

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025											
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3		
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul	
SWA GUB DEN		601d	17-Feb-23 A	16-Jun-25	0d																								
GUB		601d	17-Feb-23 A	16-Jun-25	0d																								
Summary		533d	08-May-23 A	16-Jun-25	0d																								
SUM-DUR-B	Summary - Construction (Calendar Days)	680d	08-May-23 A	11-Apr-25	-43d	Summary - Constructi																							
G-MIL-1010	*Milestone: Construction Substantial Completion (680 Calenda	0d		11-Apr-25*	-31d	*Milestone: Constructi																							
G-SUM-DUR-B10	Summary - Construction (Work Days)	472d	08-May-23 A	11-Apr-25	-31d	Summary - Constructi																							
G-CON-6870	*Milestone: Beneficial Occupancy	0d		02-May-25	30d	*Milestone: Bene																							
G-CON-6880	*Milestone: Final Completion	0d		16-Jun-25	0d	*Miles																							
Milestones		275d	23-Oct-23	20-Nov-24	20d																								
G-MIL-2000	*Milestone: Building Pad Certified Complete / Ready for Drilled	0d		23-Oct-23	-14d	*Milestone: Building Pad Certified Complete / Ready for Drilled Piers																							
G-MIL-3010	*Milestone: Drilled Pier Start	0d	24-Oct-23		-25d	*Milestone: Drilled Pier Start																							
G-MIL-3020	*Milestone: Grade Beam Start	0d	16-Nov-23		-30d	*Milestone: Grade Beam Start																							
G-MIL-3030	*Milestone: SOG Start	0d	19-Dec-23		-24d	*Milestone: SOG Start																							
G-MIL-3040	*Milestone: Tilt Wall Start	0d	23-Jan-24		-25d	*Milestone: Tilt Wall Start																							
G-MIL-2020	*Milestone: Tilt Complete (Last Panel Erection)	0d		10-May-24	-25d	*Milestone: Tilt Complete (Last Panel Erection)																							
G-MIL-3050	*Milestone: Structural Steel Start	0d	15-May-24		-27d	*Milestone: Structural Steel Start																							
G-MIL-2040	*Milestone: Steel Complete	0d		04-Jun-24	-5d	*Milestone: Steel Complete																							
G-MIL-3060	*Milestone: Interior Fit-Out Start	0d	17-Jun-24		-1d	*Milestone: Interior Fit-Out Start																							
G-MIL-2030	*Milestone: Building Dry-In	0d		27-Aug-24	4d	*Milestone: Building Dry-In																							
G-MIL-2010	*Milestone: SOGs Complete	0d		03-Sep-24	-6d	*Milestone: SOGs Complete																							
G-MIL-2060	*Milestone: Permanent Power Established	0d		20-Nov-24	20d	*Milestone: Permanent Power Established																							
Preconstruction & Design		463d	17-Feb-23 A	27-Nov-24	21d																								
Design		395d	02-May-23 A	27-Nov-24	21d																								
G-PREC-N1180	Ghafari - Design - 100% (After Permit Review)	10d	09-Oct-23	20-Oct-23	12d	Ghafari - Design - 100% (After Permit Review)																							
FRAGNET 02 - Drawing Release 07 & 16		26d	22-Sep-23 A	30-Oct-23	195d																								
G-FRG-02-1020	Owner Review and Approval - DR 07 & 16	15d	22-Sep-23 A	26-Sep-23	209d	Owner Review and Approval - DR 07 & 16																							
G-FRG-02-1030	Additional Site Storm Drain - DR 07 & 16	10d	17-Oct-23	30-Oct-23	195d	Additional Site Storm Drain - DR 07 & 16																							
FRAGNET 05 - Drawing Release 11		313d	04-May-23 A	02-Aug-24	-14d																								
G-FRG-05-1010	McCarthy Develop Pricing - DR 11	20d	04-May-23 A	28-Sep-23	160d	McCarthy Develop Pricing - DR 11																							
G-FRG-05-1020	Owner Review and Approval - DR 11	15d	29-Sep-23	19-Oct-23	160d	Owner Review and Approval - DR 11																							
G-FRG-05-1030	Additional Electrical Overhead Conduit - DR 11	5d	09-Jul-24	15-Jul-24	-21d	Additional Electrical Overhead Conduit - DR 11																							
G-FRG-05-1040	Additional Electrical In-Wall Conduit - DR 11	5d	29-Jul-24	02-Aug-24	-14d	Additional Electrical In-Wall Conduit - DR 11																							
FRAGNET 04 - Drawing Release 10		113d	02-May-23 A	19-Oct-23	-5d																								
G-FRG-04-1010	McCarthy Develop Pricing - DR 10	20d	02-May-23 A	28-Sep-23	-5d	McCarthy Develop Pricing - DR 10																							
G-FRG-04-1020	Owner Review and Approval - DR 10	15d	29-Sep-23	19-Oct-23	-5d	Owner Review and Approval - DR 10																							
FRAGNET 06 - Drawing Release 12		393d	15-May-23 A	27-Nov-24	21d																								
G-FRG-06-1010	McCarthy Develop Pricing - DR 12	20d	15-May-23 A	03-Oct-23	-10d	McCarthy Develop Pricing - DR 12																							
G-FRG-06-1020	Owner Review and Approval - DR 12	15d	04-Oct-23	24-Oct-23	-10d	Owner Review and Approval - DR 12																							
G-FRG-06-1030	Additional Tilt Panel Shop Drawings - DR 12	15d	25-Oct-23	14-Nov-23	-10d	Additional Tilt Panel Shop Drawings - DR 12																							
G-FRG-06-1040	Additional Tilt Panel Embeds - DR 12	2d	23-Feb-24	26-Feb-24	8d	Additional Tilt Panel Embeds - DR 12																							
G-FRG-06-1050	Additional Steel Erection - DR 12	2d	22-May-24	23-May-24	-29d	Additional Steel Erection - DR 12																							
G-FRG-06-1080	Additional Framing in Adim / Entry - DR 12	3d	29-Jul-24	31-Jul-24	-23d	Additional Framing in Adim / Entry - DR 12																							
G-FRG-06-1060	Additional Time for Exterior Doors - DR 12	2d	18-Sep-24	19-Sep-24	35d	Additional Time for Exterior Doors - DR 12																							
G-FRG-06-1070	Additional Time for Stair Erection - DR 12	2d	26-Nov-24	27-Nov-24	21d	Additional Time for Stair Erection - DR 12																							
FRAGNET 08 - Drawing Release 15		15d	22-Sep-23 A	26-Sep-23	38d																								
G-FRG-08-1020	Owner Review and Approval - DR 15	15d	22-Sep-23 A	26-Sep-23	38d	Owner Review and Approval - DR 15																							
GMP		25d	23-Oct-23	28-Nov-23	12d																								
Final GMP		25d	23-Oct-23	28-Nov-23	12d																								
G-PREC-N1130	Pricing Confirmation After 100%	25d	23-Oct-23	28-Nov-23	12d	Pricing Confirmation After 100%																							

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining ...
 Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024																2025					
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
Permitting		180d	17-Feb-23 A	18-Oct-23	14d																						
Water		170d	17-Feb-23 A	04-Oct-23	14d																						
G-PREC-1240	Denver Water - Permit - Water (Includes DFD) (Needed by 8/	90d	17-Feb-23 A	29-Sep-23	14d																						
G-PREC-6230	DEN - LNTP (Water)	3d	02-Oct-23	04-Oct-23	14d																						
FRAGNET 10 - Water Permit		10d	15-Aug-23 A	29-Sep-23	14d																						
FRG-10-1010	Additional Time for Water Permit - Driving Construction Install	10d	15-Aug-23 A	29-Sep-23	14d																						
Building		40d	04-Aug-23 A	18-Oct-23	14d																						
G-PREC-1070	CCD / DEN - Permit - 90% CDs - Building Permit (Needed by 9/5/23)	40d	04-Aug-23 A	13-Oct-23	-6d																						
G-PREC-6280	DOTI - Permit - SUDP (Building) (Needed by 9/5/23)	40d	04-Aug-23 A	13-Oct-23	-6d																						
G-PREC-6250	DEN - FNTP	3d	16-Oct-23	18-Oct-23	14d																						
Procurement		383d	28-Apr-23 A	29-Oct-24	46d																						
Subcontracts		60d	28-Apr-23 A	13-Oct-23	133d																						
Priority 1		30d	28-Apr-23 A	06-Oct-23	77d																						
G-SUB-1050	Contract - Glass / Storefront	20d	28-Apr-23 A	06-Oct-23	77d																						
G-SUB-1160	Contract - Paint Booth	30d	28-Apr-23 A	06-Oct-23	11d																						
G-SUB-1360	Contract - Eaton Fluid System	30d	28-Apr-23 A	06-Oct-23	29d																						
Priority 2		40d	28-Apr-23 A	06-Oct-23	138d																						
G-SUB-1300	Contract - Doors & Hardware	40d	28-Apr-23 A	25-Sep-23	29d																						
G-SUB-1290	Contract - Warehouse Racking	40d	28-Apr-23 A	06-Oct-23	138d																						
Priority 3		60d	28-Apr-23 A	13-Oct-23	102d																						
G-SUB-1350	Contract - Illuminated Signage	60d	28-Apr-23 A	13-Oct-23	102d																						
Submittals		372d	30-May-23 A	29-Oct-24	46d																						
VFDs		162d	21-Jul-23 A	11-Mar-24	43d																						
G-PR-23-1040	Submittal Prep - VFDs	60d	21-Jul-23 A	14-Nov-23	32d																						
G-PR-23-1050	McC Review - VFDs	5d	15-Nov-23	21-Nov-23	32d																						
G-PR-23-1060	A/E Review & Approve - VFDs	10d	22-Nov-23	07-Dec-23	32d																						
G-PR-23-1070	Fab & Deliver - VFDs	65d	08-Dec-23	11-Mar-24	43d																						
Mechanical - AHUs - Aaon		272d	21-Jul-23 A	14-Aug-24	-1d																						
G-PR-23-1000	Submittal Prep - AHUs - Aaon	60d	21-Jul-23 A	14-Nov-23	-1d																						
G-PR-23-1010	McC Review - AHUs - Aaon	5d	15-Nov-23	21-Nov-23	-1d																						
G-PR-23-1020	A/E Review & Approve - AHUs - Aaon	10d	22-Nov-23	07-Dec-23	-1d																						
G-PR-23-1030	Fab & Deliver - AHUs - Aaon	175d	08-Dec-23	14-Aug-24	-1d																						
Mechanical - AHUs - Rapid Engineering		248d	23-Jun-23 A	26-Jun-24	33d																						
G-PR-23-1460	Submittal Prep - AHUs - Rapid Engineering	10d	23-Jun-23 A	30-Jan-24	33d																						
G-PR-23-1470	McC Review - AHUs - Rapid Engineering	5d	31-Jan-24	06-Feb-24	33d																						
G-PR-23-1480	A/E Review & Approve - AHUs - Rapid Engineering	10d	07-Feb-24	20-Feb-24	33d																						
G-PR-23-1450	Fab & Deliver - AHUs - Rapid Engineering	90d	21-Feb-24	26-Jun-24	33d																						
Mechanical - Computer AC Units		250d	21-Jul-23 A	15-Jul-24	37d																						
G-PR-23-1210	Submittal Prep - Computer AC Units	50d	21-Jul-23 A	13-Oct-23	37d																						
G-PR-23-1220	McC Review - Computer AC Units	5d	16-Oct-23	20-Oct-23	37d																						
G-PR-23-1230	A/E Review & Approve - Computer AC Units	10d	23-Oct-23	03-Nov-23	37d																						
G-PR-23-1200	Fab & Deliver - Computer AC Units	175d	06-Nov-23	15-Jul-24	37d																						
Mechanical - Gas Fired Boiler		125d	21-Jul-23 A	18-Jan-24	74d																						
G-PR-23-1330	Submittal Prep - Gas Fired Boiler	60d	21-Jul-23 A	20-Oct-23	49d																						
G-PR-23-1340	McC Review - Gas Fired Boiler	5d	23-Oct-23	27-Oct-23	49d																						
G-PR-23-1350	A/E Review & Approve - Gas Fired Boiler	10d	30-Oct-23	10-Nov-23	49d																						
G-PR-23-1320	Fab & Deliver - Gas Fired Boiler	45d	13-Nov-23	18-Jan-24	74d																						
Mechanical - Roof Fans		185d	21-Jul-23 A	11-Apr-24	86d																						
G-PR-23-1500	Submittal Prep - Roof Fans	60d	21-Jul-23 A	05-Dec-23	86d																						


Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining ...
 Milestone

SWA GUB DEN

INTERNAL Remaining Activities



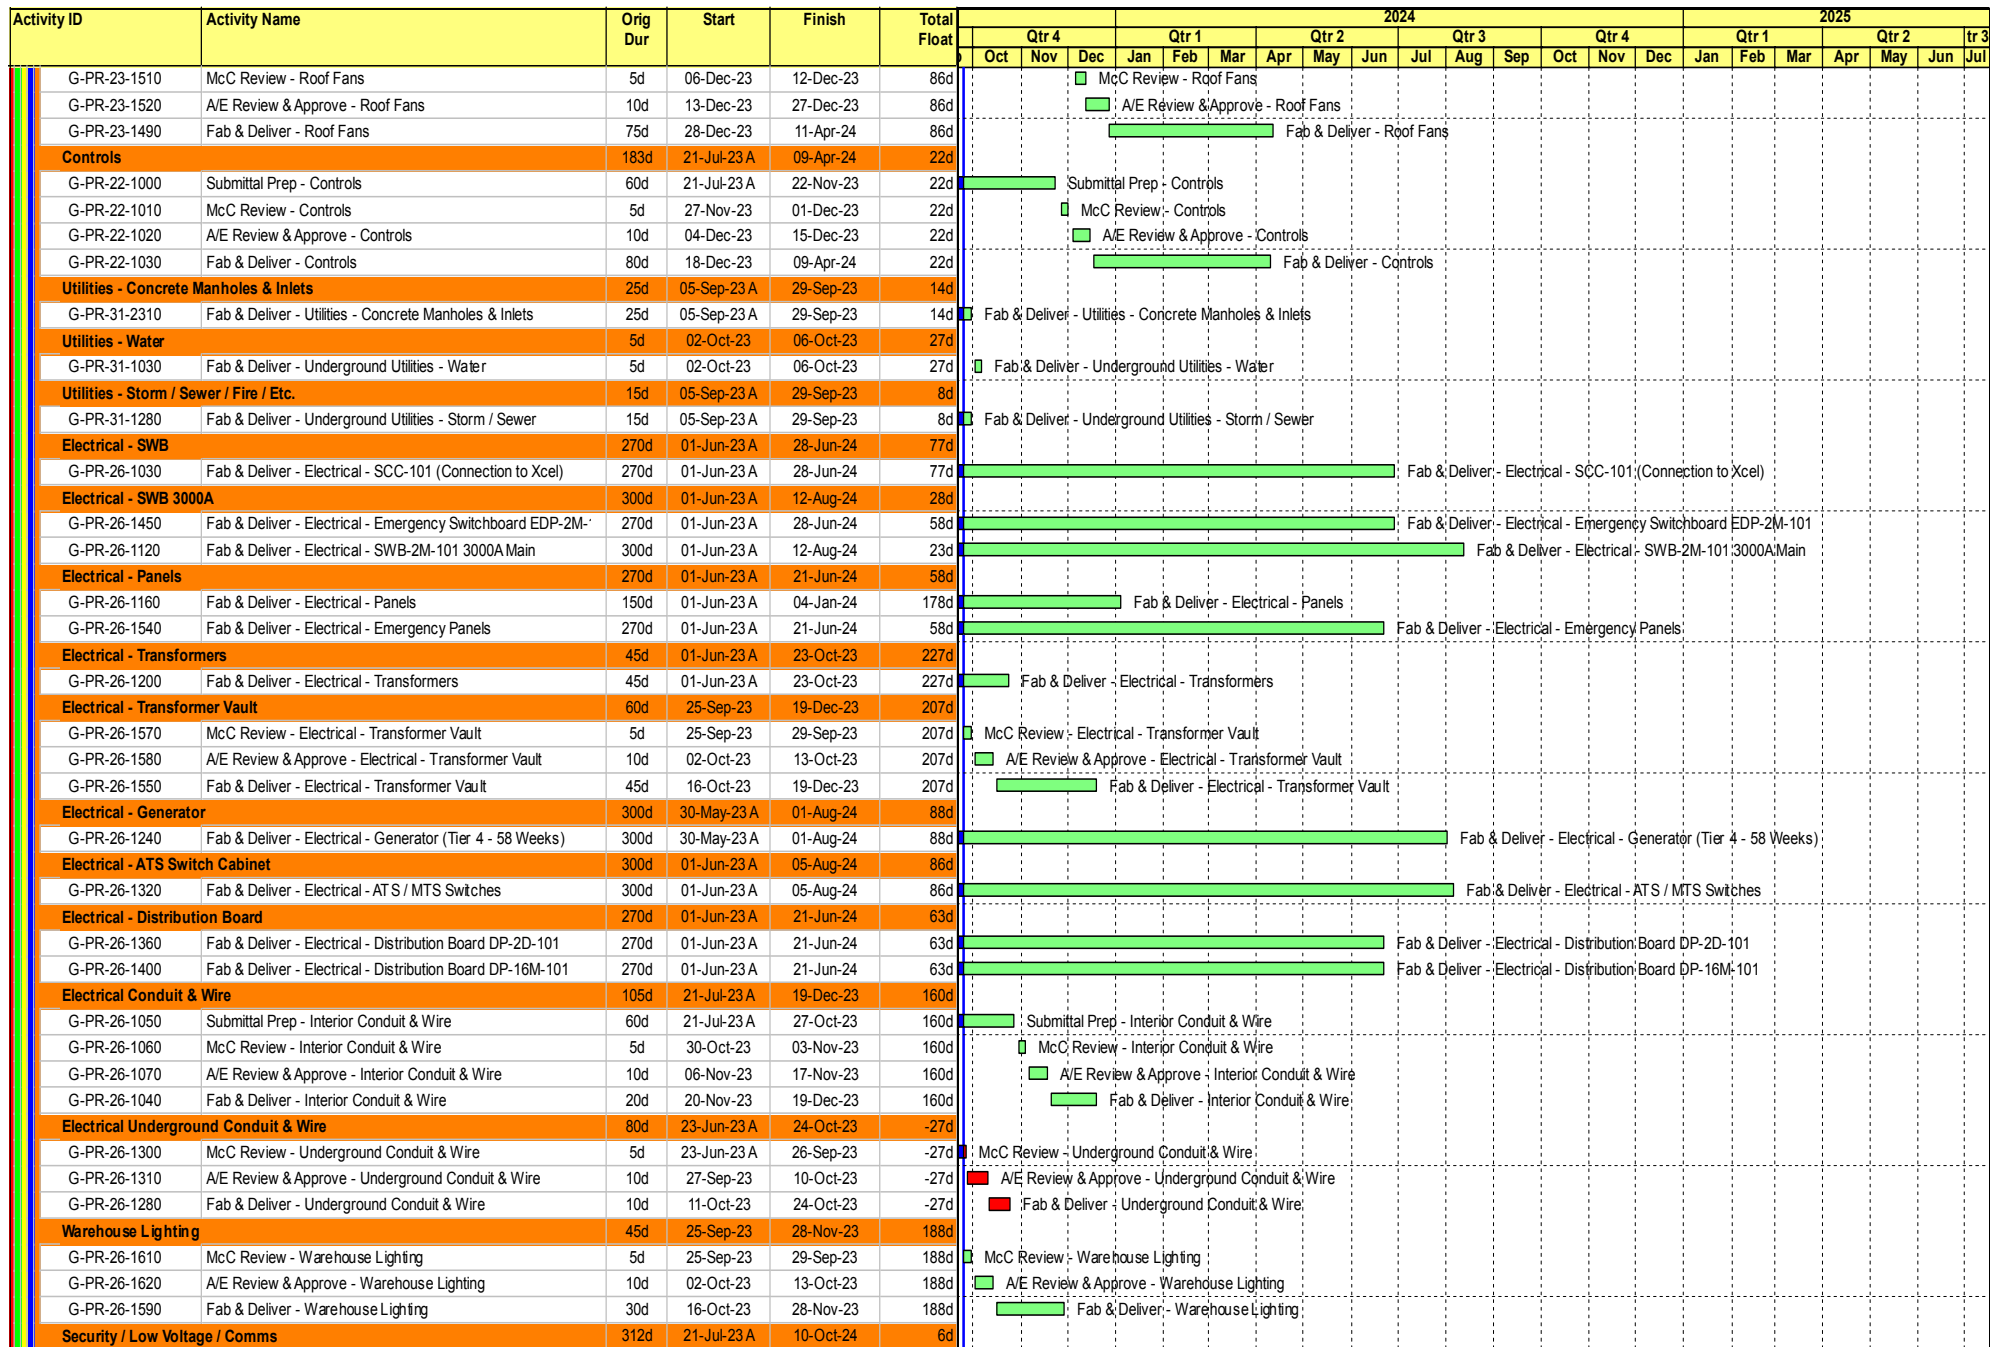







































Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
G-PR-31-1930	Submittal Prep - Security - DEN (Servitech)	35d	21-Jul-23 A	10-Oct-23	6d																						
G-PR-31-1940	McC Review - Security - DEN (Servitech)	5d	11-Oct-23	17-Oct-23	6d																						
G-PR-31-1950	A/E Review & Approve - Security - DEN (Servitech)	10d	18-Oct-23	31-Oct-23	6d																						
G-PR-31-1920	Fab & Deliver - Security - DEN (Servitech)	240d	01-Nov-23	10-Oct-24	6d																						
Underground Plumbing Pipe		20d	27-Oct-23	27-Nov-23	-30d																						
G-PR-26-1080	Fab & Deliver - Underground Plumbing Pipe	20d	27-Oct-23	27-Nov-23	-30d																						
Security - Card Readers		215d	25-Sep-23	29-Jul-24	47d																						
G-PR-31-2270	McC Review - Security - SWA (Convergent)	5d	25-Sep-23	29-Sep-23	47d																						
G-PR-31-2280	A/E Review & Approve - Security - SWA (Convergent)	10d	02-Oct-23	13-Oct-23	47d																						
G-PR-31-2290	Fab & Deliver - Security - SWA (Convergent)	200d	16-Oct-23	29-Jul-24	47d																						
Fire Suppression		203d	14-Jul-23 A	30-Apr-24	1d																						
G-PR-23-1360	BIM - Fire Suppression	30d	14-Jul-23 A	22-Nov-23	1d																						
G-PR-23-1090	Submittal Prep - Fire Suppression	25d	27-Nov-23	02-Jan-24	1d																						
G-PR-23-1100	McC Review - Fire Suppression	5d	03-Jan-24	09-Jan-24	1d																						
G-PR-23-1110	A/E Review & Approve - Fire Suppression	10d	10-Jan-24	23-Jan-24	1d																						
G-PREC-6400	Deferred Submittal - Fire Suppression	60d	24-Jan-24	16-Apr-24	1d																						
G-PR-23-1080	Fab & Deliver - Fire Suppression	10d	17-Apr-24	30-Apr-24	1d																						
Fire Pump		160d	15-Aug-23 A	01-Apr-24	122d																						
G-PR-23-1380	Submittal Prep - Fire Pump	35d	15-Aug-23 A	17-Oct-23	-7d																						
G-PR-23-1390	McC Review - Fire Pump	5d	18-Oct-23	24-Oct-23	122d																						
G-PR-23-1400	A/E Review & Approve - Fire Pump	10d	25-Oct-23	07-Nov-23	122d																						
G-PR-23-1370	Fab & Deliver - Fire Pump	100d	08-Nov-23	01-Apr-24	122d																						
ZRF Fire Sprinkler Head		179d	15-Aug-23 A	26-Apr-24	84d																						
G-PR-23-1420	Submittal Prep - ZRF Fire Sprinkler Head	60d	15-Aug-23 A	13-Dec-23	84d																						
G-PR-23-1430	McC Review - ZRF Fire Sprinkler Head	5d	14-Dec-23	20-Dec-23	84d																						
G-PR-23-1440	A/E Review & Approve - ZRF Fire Sprinkler Head	10d	21-Dec-23	05-Jan-24	84d																						
G-PR-23-1410	Fab & Deliver - ZRF Fire Sprinkler Head	80d	08-Jan-24	26-Apr-24	84d																						
Fire Alarm		205d	21-Jul-23 A	09-May-24	110d																						
G-PR-23-1130	Submittal Prep - Fire Alarm	60d	21-Jul-23 A	27-Oct-23	110d																						
G-PR-23-1140	McC Review - Fire Alarm	5d	30-Oct-23	03-Nov-23	110d																						
G-PR-23-1150	A/E Review & Approve - Fire Alarm	10d	06-Nov-23	17-Nov-23	110d																						
G-PREC-6420	Deferred Submittal - Fire Alarm & Signaling	60d	20-Nov-23	15-Feb-24	110d																						
G-PREC-6430	Deferred Submittal - Fire Alarm & Signaling: Zinwave (Radio Enhansment System)	60d	20-Nov-23	15-Feb-24	110d																						
G-PR-23-1120	Fab & Deliver - Fire Alarm	60d	16-Feb-24	09-May-24	110d																						
Concrete Mix Design - Grade Beams & Pier Caps		41d	30-Aug-23 A	26-Oct-23	-17d																						
G-PR-31-1140	McC Review - Concrete Mix Design - Grade Beams & Pier Caps	3d	30-Aug-23 A	05-Oct-23	-17d																						
G-PR-31-1150	A/E Review & Approve - Concrete Mix Design - Grade Beams & Pier Caps	10d	06-Oct-23	19-Oct-23	-17d																						
G-PR-31-1120	Fab & Deliver - Concrete - Grade Beams & Pier Caps	5d	20-Oct-23	26-Oct-23	-17d																						
Concrete Mix Design - SOG / SOD		41d	30-Aug-23 A	26-Oct-23	28d																						
G-PR-31-2660	McC Review - Concrete Mix Design - SOG / SOD	3d	30-Aug-23 A	05-Oct-23	28d																						
G-PR-31-2670	A/E Review & Approve - Concrete Mix Design - SOG / SOD	10d	06-Oct-23	19-Oct-23	28d																						
G-PR-31-2640	Fab & Deliver - Concrete - SOG / SOD	5d	20-Oct-23	26-Oct-23	28d																						
Concrete Mix Design - Tilt Panels		41d	30-Aug-23 A	26-Oct-23	31d																						
G-PR-31-2700	McC Review - Concrete Mix Design - Tilt Panels	3d	30-Aug-23 A	05-Oct-23	31d																						
G-PR-31-2710	A/E Review & Approve - Concrete Mix Design - Tilt Panels	10d	06-Oct-23	19-Oct-23	31d																						
G-PR-31-2680	Fab & Deliver - Concrete - Tilt Panels	5d	20-Oct-23	26-Oct-23	31d																						
Drilled Piers		10d	06-Oct-23	19-Oct-23	-31d																						
G-PR-31-2200	Fab & Deliver - Drilled Piers	10d	06-Oct-23	19-Oct-23	-31d																						
Rebar Shop Dwgs - Grade Beams		50d	24-Aug-23 A	02-Nov-23	-22d																						

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining ...
 Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024																		2025					
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3		
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul	
	G-PR-31-1180	McC Review - Rebar Shop Dwgs - Grade Beams	5d	24-Aug-23 A	05-Oct-23	-22d																							
	G-PR-31-1190	A/E Review & Approve - Rebar Shop Dwgs - Grade Beams	10d	06-Oct-23	19-Oct-23	-22d																							
	G-PR-31-1160	Fab & Deliver - Rebar - Grade Beams	10d	20-Oct-23	02-Nov-23	-22d																							
	Tilt Panels		10d	21-Sep-23 A	06-Oct-23	17d																							
	G-PR-31-2470	A/E Review & Approve - Tilt Panels (Product Data)	10d	21-Sep-23 A	06-Oct-23	17d																							
	SOG & Grade Beams - Anchor Bolts & Embeds		45d	21-Jul-23 A	17-Nov-23	5d																							
	G-PR-05-1320	Fab & Deliver - SOG & Grade Beams Anchor Bolts & Embeds	45d	21-Jul-23 A	17-Nov-23	5d																							
	Tilt Panel - Embeds		45d	15-Aug-23 A	01-Dec-23	9d																							
	G-PR-05-1360	Fab & Deliver - Tilt Panels Embeds	45d	15-Aug-23 A	01-Dec-23	9d																							
	Structural Steel - Joists & Decking		155d	21-Jul-23 A	29-Feb-24	26d																							
	G-PR-05-1010	McC Review - Steel Joists & Decking	6d	21-Jul-23 A	20-Oct-23	-23d																							
	G-PR-05-1020	A/E Review & Approve - Steel Joists & Decking	10d	23-Oct-23	03-Nov-23	-23d																							
	G-PR-05-1030	Fab & Deliver - Steel Joists & Decking	80d	06-Nov-23	29-Feb-24	26d																							
	Structural Steel - Columns & Beams		113d	22-Sep-23 A	29-Feb-24	20d																							
	G-PR-05-1250	McC Review - Columns & Beams	10d	22-Sep-23 A	20-Oct-23	20d																							
	G-PR-05-1260	A/E Review & Approve - Columns & Beams	10d	23-Oct-23	03-Nov-23	20d																							
	G-PR-05-1270	Fab & Deliver - Columns & Beams	80d	06-Nov-23	29-Feb-24	20d																							
	Insulated Core Metal Panels		134d	28-Aug-23 A	07-Mar-24	100d																							
	G-PR-05-1090	Submittal Prep - Insulated Core Metal Panels	50d	28-Aug-23 A	13-Oct-23	86d																							
	G-PR-05-1100	McC Review - Insulated Core Metal Panels	5d	16-Oct-23	20-Oct-23	86d																							
	G-PR-05-1110	A/E Review & Approve - Insulated Core Metal Panels	10d	23-Oct-23	03-Nov-23	86d																							
	G-PR-05-1160	Fab & Deliver - Insulated Core Metal Panels	85d	06-Nov-23	07-Mar-24	100d																							
	Masonry		135d	25-Sep-23	04-Apr-24	70d																							
	G-PR-05-1200	Submittal Prep - Masonry	60d	25-Sep-23	19-Dec-23	70d																							
	G-PR-05-1210	McC Review - Masonry	5d	20-Dec-23	27-Dec-23	70d																							
	G-PR-05-1220	A/E Review & Approve - Masonry	10d	28-Dec-23	11-Jan-24	70d																							
	G-PR-05-1190	Fab & Deliver - Masonry	60d	12-Jan-24	04-Apr-24	70d																							
	Roofing Material		20d	24-May-24	21-Jun-24	-15d																							
	G-PR-07-1030	Fab & Deliver - Roofing Material	20d	24-May-24	21-Jun-24	-15d																							
	Roofing Shop Dwgs		55d	15-Aug-23 A	31-Oct-23	148d																							
	G-PR-07-1050	Submittal Prep - Roofing Shop Dwgs	30d	15-Aug-23 A	10-Oct-23	148d																							
	G-PR-07-1060	McC Review - Roofing Shop Dwgs	5d	11-Oct-23	17-Oct-23	148d																							
	G-PR-07-1070	A/E Review & Approve - Roofing Shop Dwgs	10d	18-Oct-23	31-Oct-23	148d																							
	Glass / Aluminum Storefront		88d	09-Oct-23	13-Feb-24	77d																							
	G-PR-08-1000	Submittal Prep - Glass / Aluminum Storefront	15d	09-Oct-23	27-Oct-23	77d																							
	G-PR-08-1010	McC Review - Glass / Aluminum Storefront	5d	26-Oct-23	01-Nov-23	77d																							
	G-PR-08-1020	A/E Review & Approve - Glass / Aluminum Storefront	10d	02-Nov-23	15-Nov-23	77d																							
	G-PR-08-1030	Fab & Deliver - Glass / Aluminum Storefront	60d	16-Nov-23	13-Feb-24	77d																							
	G-PRECN-6410	Deferred Submittal - Exterior Window Wall System	60d	16-Nov-23	13-Feb-24	77d																							
	Illuminated Signage		195d	16-Oct-23	22-Jul-24	102d																							
	G-PRCR-9020	Submittal Prep - Illuminated Signage	60d	16-Oct-23	11-Jan-24	102d																							
	G-PRCR-9030	McC Review - Illuminated Signage	5d	12-Jan-24	18-Jan-24	102d																							
	G-PRCR-9040	A/E Review & Approve - Illuminated Signage	10d	19-Jan-24	01-Feb-24	102d																							
	G-PRCR-9010	Fab & Deliver - Illuminated Signage	120d	02-Feb-24	22-Jul-24	102d																							
	Custom Coiling Doors		238d	21-Jul-23 A	02-Aug-24	45d																							
	G-PR-31-1760	Design Custom Coiling Doors	125d	21-Jul-23 A	17-Jan-24	45d																							
	G-PR-31-1560	Wind Load Testing	10d	18-Jan-24	31-Jan-24	45d																							
	G-PR-31-1050	Submittal Prep - Custom Coiling Doors	15d	01-Feb-24	21-Feb-24	45d																							
	G-PR-31-1060	McC Review - Custom Coiling Doors	5d	22-Feb-24	28-Feb-24	45d																							


Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



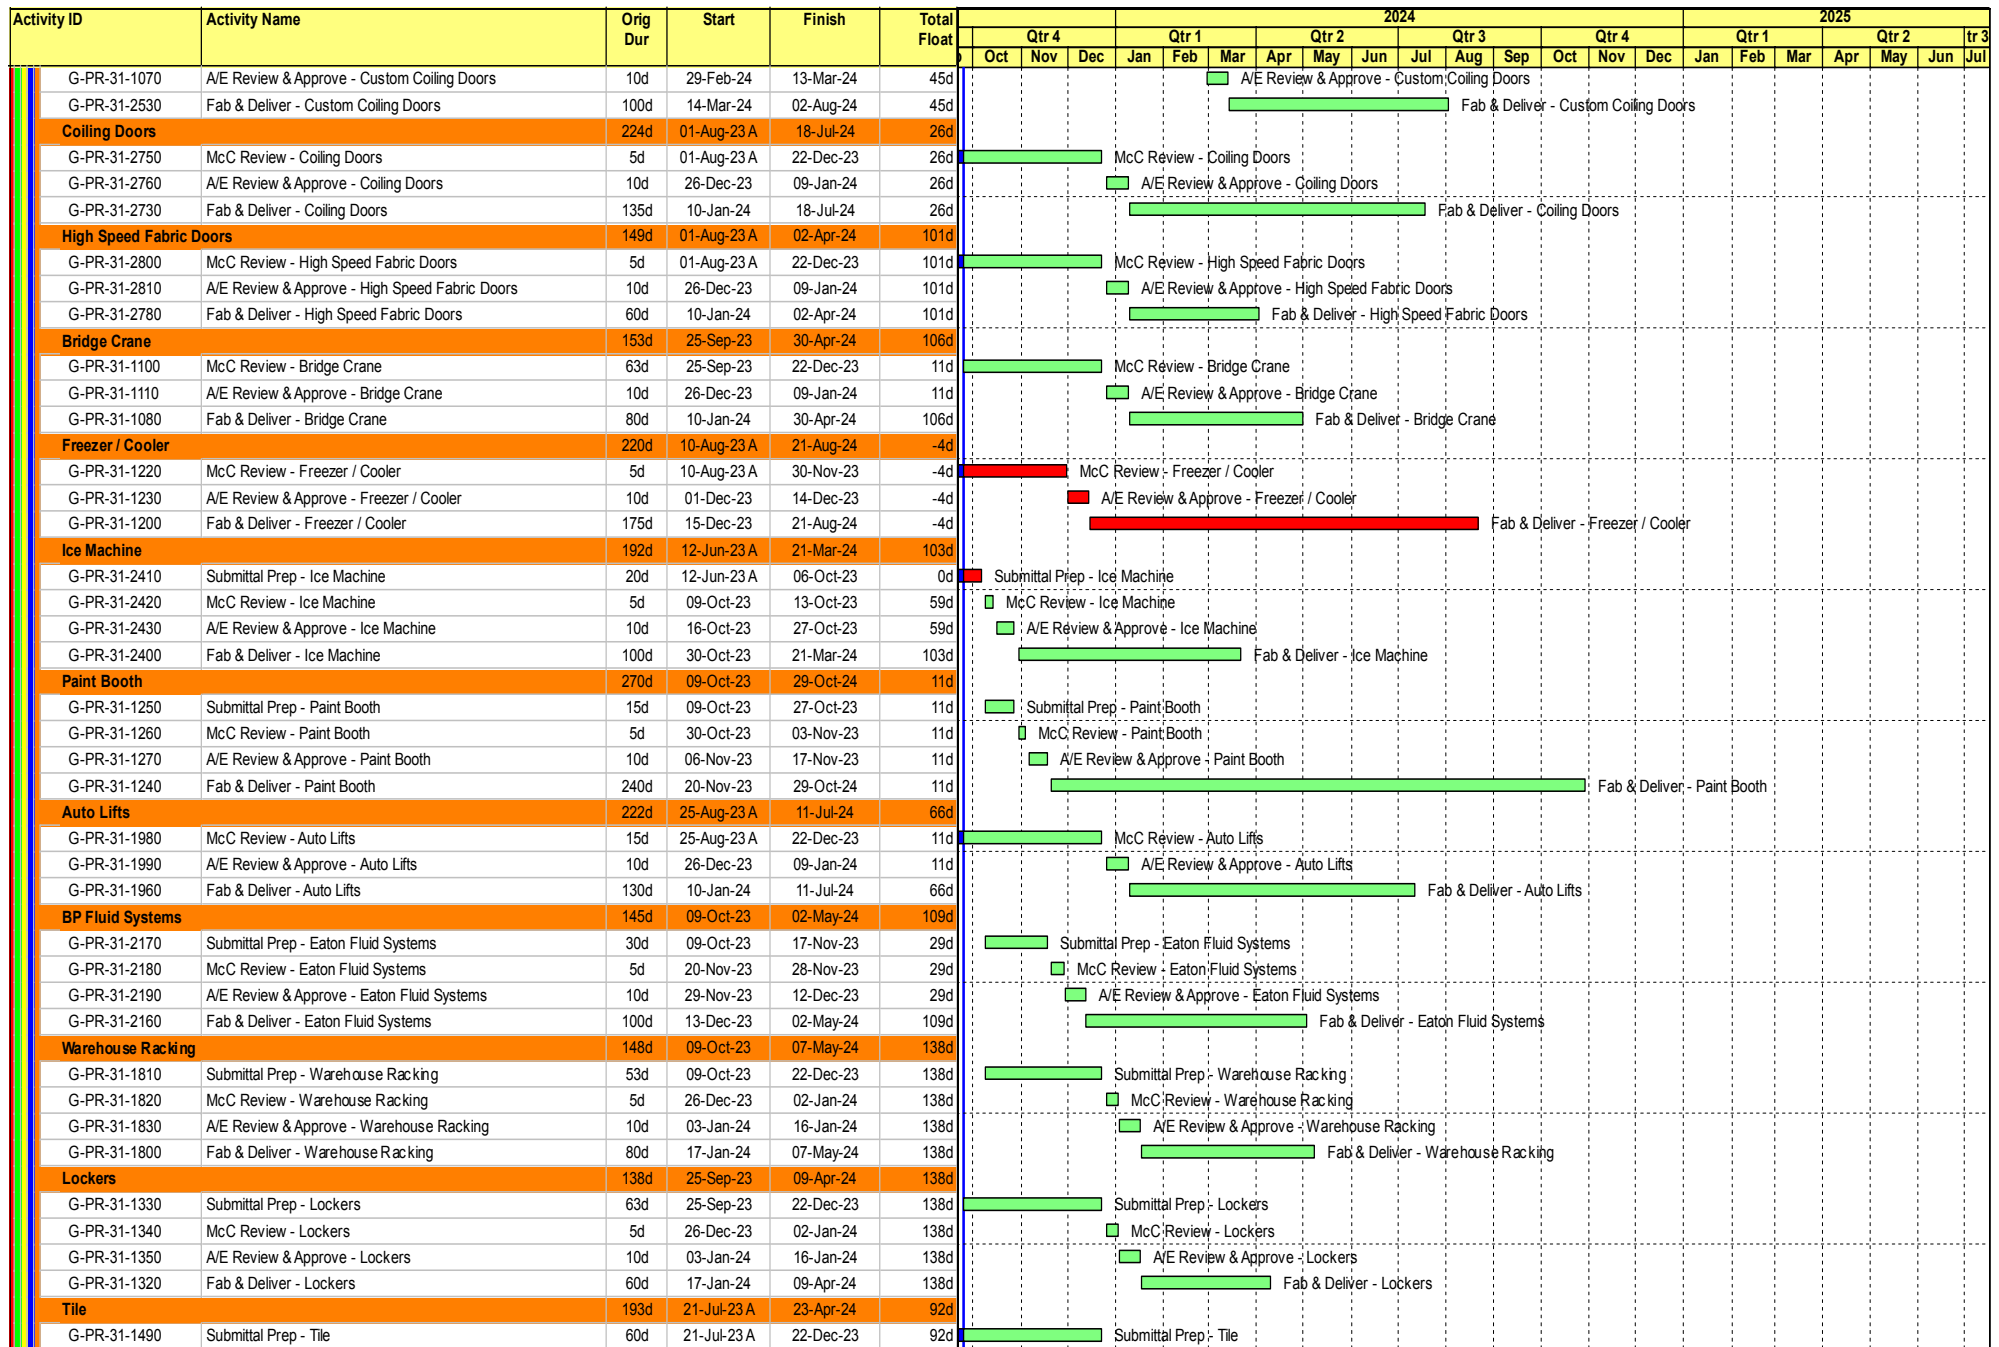

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort
 Remaining Work

 Actual Level of Effort
 Critical Remaining ...

 Actual Work
 Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024																		2025					
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3		
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul	
	G-PR-31-1500	McC Review - Tile	5d	26-Dec-23	02-Jan-24	92d																							
	G-PR-31-1510	A/E Review & Approve - Tile	10d	03-Jan-24	16-Jan-24	92d																							
	G-PR-31-1480	Fab & Deliver - Tile	70d	17-Jan-24	23-Apr-24	92d																							
	Carpet		203d	21-Jul-23 A	07-May-24	119d																							
	G-PR-31-1530	Submittal Prep - Carpet	60d	21-Jul-23 A	22-Dec-23	119d																							
	G-PR-31-1540	McC Review - Carpet	5d	26-Dec-23	02-Jan-24	119d																							
	G-PR-31-1550	A/E Review & Approve - Carpet	10d	03-Jan-24	16-Jan-24	119d																							
	G-PR-31-1520	Fab & Deliver - Carpet	80d	17-Jan-24	07-May-24	119d																							
	Concrete Seal		100d	21-Jul-23 A	12-Dec-23	261d																							
	G-PR-31-1570	Submittal Prep - Concrete Seal	60d	21-Jul-23 A	27-Oct-23	261d																							
	G-PR-31-1580	McC Review - Concrete Seal	5d	30-Oct-23	03-Nov-23	261d																							
	G-PR-31-1590	A/E Review & Approve - Concrete Seal	10d	06-Nov-23	17-Nov-23	261d																							
	G-PR-31-2040	Fab & Deliver - Concrete Seal	15d	20-Nov-23	12-Dec-23	261d																							
	Misc Metals		125d	21-Jul-23 A	18-Jan-24	232d																							
	G-PR-31-1610	Submittal Prep - Misc Metals	60d	21-Jul-23 A	27-Oct-23	232d																							
	G-PR-31-1620	McC Review - Misc Metals	5d	30-Oct-23	03-Nov-23	232d																							
	G-PR-31-1630	A/E Review & Approve - Misc Metals	10d	06-Nov-23	17-Nov-23	232d																							
	G-PR-31-1600	Fab & Deliver - Misc Metals	40d	20-Nov-23	18-Jan-24	232d																							
	Interior Fencing		130d	21-Jul-23 A	25-Jan-24	241d																							
	G-PR-31-2070	Submittal Prep - Interior Fencing	60d	21-Jul-23 A	03-Nov-23	241d																							
	G-PR-31-2080	McC Review - Interior Fencing	5d	06-Nov-23	10-Nov-23	241d																							
	G-PR-31-2090	A/E Review & Approve - Interior Fencing	10d	13-Nov-23	28-Nov-23	241d																							
	G-PR-31-2060	Fab & Deliver - Interior Fencing	40d	29-Nov-23	25-Jan-24	241d																							
	AOA / Exterior Fencing		125d	21-Jul-23 A	18-Jan-24	227d																							
	G-PR-31-2830	Submittal Prep - AOA / Exterior Fencing	60d	21-Jul-23 A	27-Oct-23	227d																							
	G-PR-31-2840	McC Review - AOA / Exterior Fencing	5d	30-Oct-23	03-Nov-23	227d																							
	G-PR-31-2850	A/E Review & Approve - AOA / Exterior Fencing	10d	06-Nov-23	17-Nov-23	227d																							
	G-PR-31-2820	Fab & Deliver - AOA / Exterior Fencing	40d	20-Nov-23	18-Jan-24	227d																							
	Specialties		148d	25-Sep-23	23-Apr-24	107d																							
	G-PR-31-1690	Submittal Prep - Specialties	63d	25-Sep-23	22-Dec-23	107d																							
	G-PR-31-1700	McC Review - Specialties	5d	26-Dec-23	02-Jan-24	107d																							
	G-PR-31-1710	A/E Review & Approve - Specialties	10d	03-Jan-24	16-Jan-24	107d																							
	G-PR-31-1680	Fab & Deliver - Specialties	70d	17-Jan-24	23-Apr-24	107d																							
	Millwork / Cabinets		148d	25-Sep-23	23-Apr-24	97d																							
	G-PR-31-1730	Submittal Prep - Millwork / Cabinets	63d	25-Sep-23	22-Dec-23	97d																							
	G-PR-31-1740	McC Review - Millwork / Cabinets	5d	26-Dec-23	02-Jan-24	97d																							
	G-PR-31-1750	A/E Review & Approve - Millwork / Cabinets	10d	03-Jan-24	16-Jan-24	97d																							
	G-PR-31-1720	Fab & Deliver - Millwork / Cabinets	70d	17-Jan-24	23-Apr-24	97d																							
	Doors & Hardware		177d	26-Sep-23	05-Jun-24	81d																							
	G-PR-31-1850	Submittal Prep - Doors & Hardware	62d	26-Sep-23	22-Dec-23	81d																							
	G-PR-31-1860	McC Review - Doors & Hardware	5d	26-Dec-23	02-Jan-24	81d																							
	G-PR-31-1870	A/E Review & Approve - Doors & Hardware	10d	03-Jan-24	16-Jan-24	81d																							
	G-PR-31-1840	Fab & Deliver - Doors & Hardware	100d	17-Jan-24	05-Jun-24	81d																							
	Door Frames		157d	26-Sep-23	07-May-24	29d																							
	G-PR-31-1890	Submittal Prep - Door Frames	62d	26-Sep-23	22-Dec-23	29d																							
	G-PR-31-1900	McC Review - Door Frames	5d	26-Dec-23	02-Jan-24	29d																							
	G-PR-31-1910	A/E Review & Approve - Door Frames	10d	03-Jan-24	16-Jan-24	29d																							
	G-PR-31-1880	Fab & Deliver - Door Frames	80d	17-Jan-24	07-May-24	29d																							
	Dock Levelers		246d	06-Jun-23 A	23-May-24	116d																							

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024																2025					
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
G-PR-31-2010	Submittal Prep - Dock Levelers	20d	06-Jun-23 A	20-Oct-23	-10d																						
G-PR-31-2020	McC Review - Dock Levelers	10d	23-Oct-23	03-Nov-23	116d																						
G-PR-31-2030	A/E Review & Approve - Dock Levelers	10d	06-Nov-23	17-Nov-23	116d																						
G-PR-31-2000	Fab & Deliver - Dock Levelers	130d	20-Nov-23	23-May-24	116d																						
Asphalt		105d	21-Jul-23 A	19-Dec-23	231d																						
G-PR-31-1370	Submittal Prep - Asphalt	60d	21-Jul-23 A	27-Oct-23	231d																						
G-PR-31-1380	McC Review - Asphalt	5d	30-Oct-23	03-Nov-23	231d																						
G-PR-31-1390	A/E Review & Approve - Asphalt	10d	06-Nov-23	17-Nov-23	231d																						
G-PR-31-1360	Fab & Deliver - Asphalt	20d	20-Nov-23	19-Dec-23	231d																						
Striping		165d	21-Jul-23 A	14-Mar-24	171d																						
G-PR-31-1650	Submittal Prep - Striping	60d	21-Jul-23 A	27-Oct-23	171d																						
G-PR-31-1660	McC Review - Striping	5d	30-Oct-23	03-Nov-23	171d																						
G-PR-31-1670	A/E Review & Approve - Striping	10d	06-Nov-23	17-Nov-23	171d																						
G-PR-31-1640	Fab & Deliver - Striping	80d	20-Nov-23	14-Mar-24	171d																						
Site Concrete		115d	21-Jul-23 A	04-Jan-24	216d																						
G-PR-31-1410	Submittal Prep - Site Concrete	60d	21-Jul-23 A	27-Oct-23	216d																						
G-PR-31-1420	McC Review - Site Concrete	5d	30-Oct-23	03-Nov-23	216d																						
G-PR-31-1430	A/E Review & Approve - Site Concrete	10d	06-Nov-23	17-Nov-23	216d																						
G-PR-31-1400	Fab & Deliver - Site Concrete	30d	20-Nov-23	04-Jan-24	216d																						
Landscaping		135d	25-Sep-23	04-Apr-24	186d																						
G-PR-31-1450	Submittal Prep - Landscaping	60d	25-Sep-23	19-Dec-23	186d																						
G-PR-31-1460	McC Review - Landscaping	5d	20-Dec-23	27-Dec-23	186d																						
G-PR-31-1470	A/E Review & Approve - Landscaping	10d	28-Dec-23	11-Jan-24	186d																						
G-PR-31-1440	Fab & Deliver - Landscaping	60d	12-Jan-24	04-Apr-24	186d																						
VDC Modeling		167d	21-Aug-23 A	16-Apr-24	11d																						
SOG		30d	09-Oct-23	17-Nov-23	-10d																						
G-VDC-1040	Incorporate Approved Material into SOG Model (Pipe, Fittings, Etc.)	10d	09-Oct-23	20-Oct-23	-10d																						
G-VDC-1050	Finalize Model / Develop Shop Dwgs for SOG	10d	23-Oct-23	03-Nov-23	-10d																						
G-VDC-1140	A/E Review & Approve Shop Dwgs for SOG	10d	06-Nov-23	17-Nov-23	-10d																						
Tilt Panels		104d	21-Aug-23 A	18-Jan-24	-23d																						
G-PR-31-2720	Rebar Shop Dwgs for Tilt Panels	14d	21-Aug-23 A	05-Oct-23	-2d																						
G-VDC-1220	Incorporate Approved Material into Tilt Panels Model	10d	06-Nov-23	17-Nov-23	-23d																						
G-VDC-1230	Finalize Model / Develop Shop Dwgs for Tilt Panels	10d	20-Nov-23	05-Dec-23	-23d																						
G-VDC-1240	A/E Review & Approve Shop Dwgs for Tilt Panels	10d	06-Dec-23	19-Dec-23	-23d																						
G-PR-31-2520	Fab & Deliver - Tilt Panel Rebar / Insulation / Accessories	20d	20-Dec-23	18-Jan-24	-23d																						
Interior Fitout		70d	10-Jan-24	16-Apr-24	11d																						
G-VDC-1100	Incorporate Approved Material into Model for Interior Fitout	40d	10-Jan-24	05-Mar-24	11d																						
G-VDC-1120	Clash Coordination w/ Trades for Interior Fitout	10d	06-Mar-24	19-Mar-24	11d																						
G-VDC-1110	Finalize Model / Develop Shop Dwgs for Interior Fitout	10d	20-Mar-24	02-Apr-24	11d																						
G-VDC-1160	A/E Review & Approve Shop Dwgs for Interior Fitout	10d	03-Apr-24	16-Apr-24	11d																						
Construction		449d	12-Jun-23 A	02-May-25	30d																						
Earthwork		71d	12-Jun-23 A	06-Nov-23	206d																						
G-CON-6250	North Building Underdrain - Lift 2 - 524 LF (Grid J-A)	6d	22-Sep-23 A	28-Sep-23	-28d																						
G-CON-7800	Plumbing Sleeves at Underdrain - Building South	10d	18-Sep-23 A	29-Sep-23	-22d																						
G-CON-6930	Plumbing Sleeves at Underdrain - Building North	5d	29-Sep-23	05-Oct-23	-7d																						
G-CON-1470	Fill from Stockpile South Fill 2 Building & Region 7 - 1,900 CY's	1d	17-Oct-23	17-Oct-23	-15d																						
G-CON-1480	Certify Building Pad - North & Parking Areas	4d	18-Oct-23	23-Oct-23	-15d																						
FRAGNET 01 - New Geo-Technical Requirements		71d	12-Jun-23 A	06-Nov-23	206d																						
G-FRG-01-1280	Cut Region 8 to 6 - 7,900 CY's	4d	21-Sep-23 A	25-Sep-23	-31d																						

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
G-FRG-01-1430	Jviation & GEG Coordinate for Direction at Failed Areas	10d	22-Sep-23	A	25-Sep-23	-25d	Jviation & GEG Coordinate for Direction at Failed Areas																				
G-FRG-01-1180	Take Swell Test #2 of Stockpile South (South Ribbon) after 10I	10d	28-Aug-23	A	26-Sep-23	-31d	Take Swell Test #2 of Stockpile South (South Ribbon) after 10K CY's Place and Processed																				
G-FRG-01-1390	Region 7 Cut to Fill 3 - 2,400 CY's	1d	26-Sep-23		26-Sep-23	-31d	Region 7 Cut to Fill 3 - 2,400 CY's																				
G-FRG-01-1230	South Building Underdrain - Lift 2 - 1335 LF - (Grid J-R)	8d	14-Sep-23	A	29-Sep-23	-30d	South Building Underdrain - Lift 2 - 1335 LF - (Grid J-R)																				
G-FRG-01-1050	Owner Review and Approval Pricing - New Geo Tech Require	15d	21-Jul-23	A	02-Oct-23	31d	Owner Review and Approval Pricing - New Geo Tech Requirements																				
G-FRG-01-1250	Region 8 Cut to Fill 3 - 9,400 CY's (Region South)	5d	27-Sep-23		03-Oct-23	-31d	Region 8 Cut to Fill 3 - 9,400 CY's (Region South)																				
G-FRG-01-1420	Rework Top 2 Ft of Area 1B & Region 2	3d	29-Sep-23		03-Oct-23	-28d	Rework Top 2 Ft of Area 1B & Region 2																				
G-FRG-01-1220	Fill from Stockpile South to Fill 1 Building - 16,500 CY's - Buildi	7d	04-Oct-23		12-Oct-23	-31d	Fill from Stockpile South to Fill 1 Building - 16,500 CY's - Building Pad																				
G-FRG-01-1400	Fill from Stockpile South to Fill 2 Building - 2,900 CY's - N Bulc	2d	13-Oct-23		16-Oct-23	-15d	Fill from Stockpile South to Fill 2 Building - 2,900 CY's - N Building Pad																				
G-FRG-01-1340	Cut Region 8 to Fill 7 - 2,100 CY's	1d	18-Oct-23		18-Oct-23	15d	Cut Region 8 to Fill 7 - 2,100 CY's																				
G-FRG-01-1300	Certify Building Pad - South & Parking Area	5d	13-Oct-23		19-Oct-23	-31d	Certify Building Pad - South & Parking Area																				
G-FRG-01-1060	Additional Earthwork - Stockpile & Over Excavation & Fill Site	31d	12-Jun-23	A	24-Oct-23	15d	Additional Earthwork - Stockpile & Over Excavation & Fill Site																				
G-FRG-01-1350	Cut Region 9 to Fill 7 - 9,500 CY's	4d	19-Oct-23		24-Oct-23	15d	Cut Region 9 to Fill 7 - 9,500 CY's																				
G-FRG-01-1290	Cut Region 9 & 10 to Export / Stockpile - 7,600 CY's	3d	25-Oct-23		27-Oct-23	208d	Cut Region 9 & 10 to Export / Stockpile - 7,600 CY's																				
G-FRG-01-1360	Pond Cut to Fill Region NW - 10,866 CY's	5d	25-Oct-23		31-Oct-23	206d	Pond Cut to Fill Region NW - 10,866 CY's																				
G-FRG-01-1370	Pond/Tract to Stockpile or Cargo - 7,290 CY's	4d	01-Nov-23		06-Nov-23	206d	Pond/Tract to Stockpile or Cargo - 7,290 CY's																				
Site Utilities		289d	04-Oct-23		20-Nov-24	143d																					
Storm / Sewer / Water		192d	04-Oct-23		05-Jul-24	240d																					
Sanitary Sewer		18d	04-Oct-23		27-Oct-23	414d																					
G-CON-5125	Sanitary EX MH-1 to MH6 - 92LF+CTE+MH	2d	04-Oct-23		05-Oct-23	6d	Sanitary EX MH-1 to MH6 - 92LF+CTE+MH																				
G-CON-5145	Sanitary MH6 to MH3 - 327LF+OWS+3MH	4d	17-Oct-23		20-Oct-23	6d	Sanitary MH6 to MH3 - 327LF+OWS+3MH																				
G-CON-8390	Sanitary MH3 to MH1 - 406LF + MH	3d	23-Oct-23		25-Oct-23	6d	Sanitary MH3 to MH1 - 406LF + MH																				
G-CON-8400	Sanitary Testing	2d	26-Oct-23		27-Oct-23	414d	Sanitary Testing																				
Storm Sewer		55d	06-Oct-23		26-Dec-23	173d																					
G-CON-5135	Storm SDG South 1 - MH 1 to MH3 - 498LF+4MH	4d	06-Oct-23		11-Oct-23	6d	Storm SDG South 1 - MH 1 to MH3 - 498LF+4MH																				
G-CON-5070	Storm SDG South 1 - Laterals - 172LF+MH+3INLET	3d	12-Oct-23		16-Oct-23	6d	Storm SDG South 1 - Laterals - 172LF+MH+3INLET																				
G-CON-5270	Storm SDG West 1 - MH1 to MH13 - 253LF+4MH	4d	26-Oct-23		31-Oct-23	6d	Storm SDG West 1 - MH1 to MH13 - 253LF+4MH																				
G-CON-7790	Storm SDG North 3 - MH13 to MH27 - 456LF+4MH	4d	01-Nov-23		06-Nov-23	6d	Storm SDG North 3 - MH13 to MH27 - 456LF+4MH																				
G-CON-5155	Storm SDG North 1 - MH5 to IN10 - 390LF+2MH+2INLET	3d	07-Nov-23		09-Nov-23	6d	Storm SDG North 1 - MH5 to IN10 - 390LF+2MH+2INLET																				
G-CON-5165	Storm SDG East 1 - MH16 to MH18 - 234LF+2MH	2d	10-Nov-23		13-Nov-23	173d	Storm SDG East 1 - MH16 to MH18 - 234LF+2MH																				
G-CON-5175	Storm SDG East 2 - IN7 to IN6 - 168LF+2INLET	2d	14-Nov-23		15-Nov-23	173d	Storm SDG East 2 - IN7 to IN6 - 168LF+2INLET																				
G-CON-8410	Storm SDG East 3 - IN9 to MH20 - 168LF+2MH+INLET	2d	16-Nov-23		17-Nov-23	173d	Storm SDG East 3 - IN9 to MH20 - 168LF+2MH+INLET																				
G-CON-8420	Storm SDG West 1 - MH13 to FES - 252LF+2MH+FES	3d	20-Nov-23		22-Nov-23	173d	Storm SDG West 1 - MH13 to FES - 252LF+2MH+FES																				
G-CON-8430	Storm SDG West 3 - OS to EX IN - 366LF+2MH	4d	27-Nov-23		30-Nov-23	173d	Storm SDG West 3 - OS to EX IN - 366LF+2MH																				
G-CON-8440	Storm SDG South 1 - MH3 to FES - 340LF+MH+FES	3d	01-Dec-23		05-Dec-23	173d	Storm SDG South 1 - MH3 to FES - 340LF+MH+FES																				
G-CON-8450	Storm SGD North 1 - IN16 to MH5 - 328LF+4MH+INLET	3d	06-Dec-23		08-Dec-23	173d	Storm SGD North 1 - IN16 to MH5 - 328LF+4MH+INLET																				
G-CON-8460	Storm SDG West 2 - IN14 to IN15 - 100LF+2INLET	1d	11-Dec-23		11-Dec-23	173d	Storm SDG West 2 - IN14 to IN15 - 100LF+2INLET																				
G-CON-8470	Storm SDG West 6 & SDG North 2 - 32LF+2INLET	1d	12-Dec-23		12-Dec-23	173d	Storm SDG West 6 & SDG North 2 - 32LF+2INLET																				
G-CON-8480	Storm SDG West 4 & SDG West 5 - 232LF+8FES	3d	13-Dec-23		15-Dec-23	173d	Storm SDG West 4 & SDG West 5 - 232LF+8FES																				
G-CON-8490	Storm SDG West 1 - Laterals - 81LF+2INLET	1d	18-Dec-23		18-Dec-23	173d	Storm SDG West 1 - Laterals - 81LF+2INLET																				
G-CON-8500	Storm Testing	5d	19-Dec-23		26-Dec-23	173d	Storm Testing																				
Water Main		36d	09-Oct-23		29-Nov-23	6d																					
G-CON-5090	Water STA 0+00 to 4+00 - 400LF+CTE+3 LOWER	4d	09-Oct-23		12-Oct-23	38d	Water STA 0+00 to 4+00 - 400LF+CTE+3 LOWER																				
G-CON-5860	Water STA 4+00 to 6+50 - 250LF+2 LOWER	3d	01-Nov-23		03-Nov-23	10d	Water STA 4+00 to 6+50 - 250LF+2 LOWER																				
G-CON-5220	Water STA 6+50 to 13+00 - 650LF+3 LOWER	5d	10-Nov-23		16-Nov-23	6d	Water STA 6+50 to 13+00 - 650LF+3 LOWER																				
G-CON-8530	Water STA 13+00 to 17+52 - 450LF+CTE+3 LOWER	5d	17-Nov-23		27-Nov-23	6d	Water STA 13+00 to 17+52 - 450LF+CTE+3 LOWER																				
G-CON-8540	Water 3" & 3/4" Building Services	1d	28-Nov-23		28-Nov-23	6d	Water 3" & 3/4" Building Services																				
G-CON-8550	Water Test	1d	29-Nov-23		29-Nov-23	6d	Water Test																				
Gas Ex/BF		22d	05-Jun-24		05-Jul-24	38d																					

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	G-CON-8510	Excavate Gas Main - 1000LF	6d	05-Jun-24	12-Jun-24	38d																					
	G-CON-8520	Backfill Gas Main - 1000LF	6d	27-Jun-24	05-Jul-24	38d																					
	Electrical / Gas		274d	25-Oct-23	20-Nov-24	-15d																					
	G-CON-5160	Electrical Ductbank (from Xcel Tie-in)	15d	25-Oct-23	14-Nov-23	-10d																					
	G-CON-5150	Telecom Ductbank for Fiber Optic Line	20d	15-Nov-23	14-Dec-23	-10d																					
	G-CON-5140	Xcel - Gas Line Install	10d	13-Jun-24	26-Jun-24	38d																					
	G-CON-6760	Set Transformer Vault & F/R/P Electrical Gear Pad for SCC-101	5d	24-Jun-24	28-Jun-24	77d																					
	G-CON-5130	Xcel - Electrical MV Ductbank Install	25d	07-Aug-24	11-Sep-24	26d																					
	G-CON-6750	Install SCC-101 (Feed from Xcel)	2d	12-Sep-24	13-Sep-24	26d																					
	G-CON-5170	Xcel Transformer - Set & Pull Wire	5d	16-Sep-24	20-Sep-24	26d																					
	G-CON-5180	Xcel Set Meter - After Electrical Final Interiors	2d	19-Nov-24	20-Nov-24	-15d																					
	Structure		268d	15-Aug-23 A	03-Sep-24	-5d																					
	Mockup		94d	25-Sep-23	07-Feb-24	86d																					
	Mockup Procurement		90d	25-Sep-23	01-Feb-24	87d																					
	MU-1070	MU Procure - Framing	5d	09-Oct-23	13-Oct-23	22d																					
	MU-1090	MU Procure - Paint	5d	09-Oct-23	13-Oct-23	22d																					
	MU-1040	MU Procure - Formwork	10d	09-Oct-23	20-Oct-23	17d																					
	MU-1020	MU Procure - Rebar	10d	20-Oct-23	02-Nov-23	8d																					
	MU-1110	MU Procure - Roofing	35d	25-Sep-23	10-Nov-23	2d																					
	MU-1060	MU Procure - Metal Panels & Coping Cap	10d	06-Nov-23	17-Nov-23	136d																					
	MU-1030	MU Procure - Steel	15d	06-Nov-23	28-Nov-23	1d																					
	MU-1100	MU Procure - Plumbing	54d	25-Sep-23	11-Dec-23	-10d																					
	MU-1050	MU Procure - Glazing	40d	16-Nov-23	16-Jan-24	99d																					
	MU-1080	MU Procure - Translucent Panels	60d	06-Nov-23	01-Feb-24	86d																					
	Mockup Construction		59d	13-Nov-23	07-Feb-24	86d																					
	MU-1010	MU - Excavate and Grade for footing/SOG	2d	13-Nov-23	14-Nov-23	2d																					
	MU-1120	MU - Install Rebar and Place Embeds for Grade Beam/SOG (2d	15-Nov-23	16-Nov-23	2d																					
	MU-1130	MU - P/F/C GB/SOG/Waste Slab	1d	16-Nov-23	16-Nov-23	2d																					
	MU-1140	MU - Strip, Clean, and Prep Slabs	1d	17-Nov-23	17-Nov-23	2d																					
	MU-1150	MU - Layout and Form up Tilt Panels	2d	20-Nov-23	21-Nov-23	2d																					
	MU-1160	MU - Place WWF and MEP Rough-in (Pre-Pour Inspection)	1d	12-Dec-23	12-Dec-23	-10d																					
	MU-1170	MU - P/F Architectural Pour 1 and Insulation/Pins	1d	13-Dec-23	13-Dec-23	-10d																					
	MU-1180	MU - Install Rebar, Embeds, and Pick Points for Pour 2 (Pre-F	2d	14-Dec-23	15-Dec-23	-10d																					
	MU-1190	MU - P/F/C Pour 2	3d	15-Dec-23	19-Dec-23	-10d																					
	MU-1200	MU - Weld Connections (Inspect Welds)	1d	19-Dec-23	19-Dec-23	-10d																					
	MU-1210	MU - Install Bracing for Tilt Panels	1d	20-Dec-23	20-Dec-23	-10d																					
	MU-1220	MU - Tilt Crane Mob (Assembly Inspection)	1d	21-Dec-23	21-Dec-23	-10d																					
	MU-1230	MU - Place Rigging and Erect Tilt Panels	1d	21-Dec-23	21-Dec-23	-10d																					
	MU-1250	MU - Demob Crane	1d	21-Dec-23	21-Dec-23	-10d																					
	MU-1240	MU - Weld Connections (Inspect Welds)	1d	22-Dec-23	22-Dec-23	-10d																					
	MU-1260	MU - AE Review and Sign Off on Concrete	1d	26-Dec-23	26-Dec-23	-10d																					
	MU-1270	MU - Backfill Pour Back Strip	1d	27-Dec-23	27-Dec-23	-10d																					
	MU-1280	MU - Bulkhead Pour Back Strip and P/F/C pour back (Pre-Poi	2d	27-Dec-23	28-Dec-23	-10d																					
	MU-1290	MU - Exterior Caulking	1d	29-Dec-23	29-Dec-23	105d																					
	MU-1370	MU - AE Review and Sign Off on Tilt Mockup	1d	29-Dec-23	29-Dec-23	-10d																					
	MU-1300	MU - Place Exterior Coating	1d	02-Jan-24	02-Jan-24	105d																					
	MU-1310	MU - AE Review and Sign Off on Coating	1d	03-Jan-24	03-Jan-24	110d																					
	MU-1320	MU - Install Canopy Framing and Metal Decking	2d	03-Jan-24	04-Jan-24	105d																					
	MU-1330	MU - Install Roof Drain Piping (Close-in Inspection)	1d	04-Jan-24	04-Jan-24	105d																					

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining ...
 Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025										
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3	
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul
	MU-1340	MU - Install Sheathing/Roofing System at Canopy, Trim Out Dr	1d	05-Jan-24	05-Jan-24	105d																						
	MU-1350	MU - Install Metal Panels and Coping Cap	2d	02-Feb-24	05-Feb-24	86d																						
	MU-1360	MU - Install Glazing and Translucent Panel	2d	05-Feb-24	06-Feb-24	86d																						
	MU-1380	MU - AE Review and Sign Off on Mockup w/ Exterior Finishes	1d	07-Feb-24	07-Feb-24	86d																						
	Foundations & SOG		268d	15-Aug-23 A	03-Sep-24	-6d																						
	Drilled Piers		74d	15-Aug-23 A	29-Nov-23	-17d																						
	G-CON-5060	Pre-Mob Prep for Drilled Piers (7460 Review with DEN)	20d	15-Aug-23 A	09-Oct-23	-23d																						
	G-CON-5010	Mobilize Equipment for Drilled Piers	2d	20-Oct-23	23-Oct-23	-31d																						
	G-CON-5870	Drilled Piers Sequence W1 - Grid 5-14, M-N - Orange	5d	24-Oct-23	30-Oct-23	-31d																						
	G-CON-5880	Drilled Piers Sequence W2 - Grid 10-15, M-R - Blue	5d	31-Oct-23	06-Nov-23	-30d																						
	G-CON-5890	Drilled Piers Sequence W3 - Grid 8-16, J-R - Green	5d	07-Nov-23	13-Nov-23	-30d																						
	G-CON-5900	Drilled Piers Sequence W4 - Grid 3-14, A-L Red	5d	14-Nov-23	20-Nov-23	-30d																						
	G-CON-5910	Drilled Piers Sequence W5 - Grid 1-4, A-Q Magenta	5d	21-Nov-23	29-Nov-23	-17d																						
	Earthwork for Grade Beams		48d	31-Oct-23	10-Jan-24	-27d																						
	G-CON-6350	Underground Electrical & Telecomm Ductbank Under Grade E	5d	31-Oct-23	06-Nov-23	-31d																						
	G-CON-5920	Exc / Grade 1:1 & Place ABC for GB - Drilled Piers Sequence	7d	07-Nov-23	15-Nov-23	-31d																						
	G-CON-6790	Underground Plumbing Under Grade Beams (West to East)	5d	17-Nov-23	27-Nov-23	-30d																						
	G-CON-5930	Exc / Grade 1:1 & Place ABC for GB - Drilled Piers Sequence	7d	16-Nov-23	28-Nov-23	-31d																						
	G-CON-5940	Exc / Grade 1:1 & Place ABC for GB - Drilled Piers Sequence	7d	29-Nov-23	07-Dec-23	-31d																						
	G-CON-6150	Underground Plumbing for SOG 1 Grid L-Q, 10-15	8d	28-Nov-23	07-Dec-23	-30d																						
	G-CON-5950	Exc / Grade 1:1 & Place ABC for GB - Drilled Piers Sequence	7d	08-Dec-23	18-Dec-23	-31d																						
	G-CON-8000	Underground Electrical for SOG 1 Grid L-Q, 10-15	10d	05-Dec-23	18-Dec-23	-30d																						
	G-CON-7770	Underground Plumbing for SOG 2 Grid L-Q, 10-1	8d	08-Dec-23	19-Dec-23	-28d																						
	G-CON-5960	Exc / Grade 1:1 & Place ABC for GB - Drilled Piers Sequence	7d	19-Dec-23	28-Dec-23	-30d																						
	G-CON-7780	Underground Plumbing for SOG 3 Grid Grid L-A, 6-1	8d	20-Dec-23	02-Jan-24	-23d																						
	G-CON-8010	Underground Electrical for SOG 2 Grid L-Q, 10-1	10d	19-Dec-23	03-Jan-24	-30d																						
	G-CON-8020	Underground Electrical for SOG 3 Grid Grid L-A, 6-1	5d	04-Jan-24	10-Jan-24	-27d																						
	Grade Beams		49d	16-Nov-23	29-Jan-24	102d																						
	Crew 1 - Grade Beams		49d	16-Nov-23	29-Jan-24	102d																						
	GB2 - Grid Q, 5-12		9d	16-Nov-23	30-Nov-23	-22d																						
	G-CON-1060	GB2 Layout Grade Beams - Grid Q, 5-12	1d	16-Nov-23	16-Nov-23	-31d																						
	G-CON-5210	GB2 Form One Side of GB & Install Void Form - Grid Q, 5-12	1d	17-Nov-23	17-Nov-23	-31d																						
	G-CON-5230	GB2 Install Rebar for GB - Grid Q, 5-12	2d	20-Nov-23	21-Nov-23	-24d																						
	G-CON-5970	GB2 Close Form for GB - Grid Q, 5-12	2d	21-Nov-23	22-Nov-23	-24d																						
	G-CON-5980	GB2 Install Anchor Bolts/ Clean Up - Grid Q, 5-12	2d	21-Nov-23	22-Nov-23	-24d																						
	G-CON-5990	GB2 Inspection - Grid Q, 5-12	1d	22-Nov-23	22-Nov-23	-24d																						
	G-CON-5240	GB2 Set and Pour GB - Grid Q, 5-12	3d	27-Nov-23	29-Nov-23	-22d																						
	G-CON-5260	GB2 Strip, Clean, & Move Formwork - Grid Q, 5-12	1d	30-Nov-23	30-Nov-23	-22d																						
	GB4 - Grid Q-P, 12-15		9d	28-Nov-23	08-Dec-23	-26d																						
	G-CON-5480	GB4 Layout Grade Beams - Grid Q-P, 12-15	1d	28-Nov-23	28-Nov-23	-26d																						
	G-CON-5250	GB4 Form One Side of GB & Install Void Form - Grid Q-P, 12-	1d	29-Nov-23	29-Nov-23	-26d																						
	G-CON-5280	GB4 Install Rebar for GB - Grid Q-P, 12-15	2d	30-Nov-23	01-Dec-23	-26d																						
	G-CON-6000	GB4 Close Form for GB - Grid Q-P, 12-15	2d	01-Dec-23	04-Dec-23	-26d																						
	G-CON-6010	GB4 Install Anchor Bolts/ Clean Up - Grid Q-P, 12-15	2d	01-Dec-23	04-Dec-23	-26d																						
	G-CON-6020	GB4 Inspection - Grid Q-P, 12-15	1d	04-Dec-23	04-Dec-23	-26d																						
	G-CON-5290	GB4 Set and Pour GB - Grid Q-P, 12-15	3d	05-Dec-23	07-Dec-23	-26d																						
	G-CON-5660	GB4 Strip, Clean, & Move Formwork - Grid Q-P, 12-15	1d	08-Dec-23	08-Dec-23	-26d																						
	GB6 - Grid L-N, 13-15		19d	01-Dec-23	28-Dec-23	-31d																						
	G-CON-5490	GB6 Layout Grade Beams - Grid L-N, 13-15	1d	01-Dec-23	01-Dec-23	-22d																						

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN
INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	G-CON-5300	GB6 Form One Side of GB & Install Void Form - Grid L-N, 13-	1d	08-Dec-23	08-Dec-23	-26d				I	GB6 Form One Side of GB & Install Void Form - Grid L-N, 13-15																
	G-CON-5320	GB6 Install Rebar for GB - Grid L-N, 13-15	2d	11-Dec-23	12-Dec-23	-25d				I	GB6 Install Rebar for GB - Grid L-N, 13-15																
	G-CON-5310	GB6 Close Form for GB - Grid L-N, 13-15	2d	20-Dec-23	21-Dec-23	-31d				I	GB6 Close Form for GB - Grid L-N, 13-15																
	G-CON-5350	GB6 Install Anchor Bolts/ Clean Up - Grid L-N, 13-15	2d	20-Dec-23	21-Dec-23	-31d				I	GB6 Install Anchor Bolts/ Clean Up - Grid L-N, 13-15																
	G-CON-5400	GB6 Inspection - Grid L-N, 13-15	1d	21-Dec-23	21-Dec-23	-31d				I	GB6 Inspection - Grid L-N, 13-15																
	G-CON-5340	GB6 Set and Pour GB - Grid L-N, 13-15	3d	22-Dec-23	27-Dec-23	-31d				I	GB6 Set and Pour GB - Grid L-N, 13-15																
	G-CON-5370	GB6 Strip, Clean, & Move Formwork - Grid L-N, 13-15	1d	28-Dec-23	28-Dec-23	-31d				I	GB6 Strip, Clean, & Move Formwork - Grid L-N, 13-15																
	GB8 - Grid L, 7-13		15d	11-Dec-23	02-Jan-24	-31d																					
	G-CON-7250	GB8 Layout Grade Beams - Grid L, 7-13	1d	11-Dec-23	11-Dec-23	-26d				I	GB8 Layout Grade Beams - Grid L, 7-13																
	G-CON-5330	GB8 Form One Side of GB & Install Void Form - Grid L, 7-13	1d	19-Dec-23	19-Dec-23	-31d				I	GB8 Form One Side of GB & Install Void Form - Grid L, 7-13																
	G-CON-5360	GB8 Install Rebar for GB - Grid L, 7-13	2d	20-Dec-23	21-Dec-23	-30d				I	GB8 Install Rebar for GB - Grid L, 7-13																
	G-CON-5440	GB8 Close Form for GB - Grid L, 7-13	2d	22-Dec-23	26-Dec-23	-31d				I	GB8 Close Form for GB - Grid L, 7-13																
	G-CON-6030	GB8 Install Anchor Bolts/ Clean Up - Grid L, 7-13	2d	22-Dec-23	26-Dec-23	-31d				I	GB8 Install Anchor Bolts/ Clean Up - Grid L, 7-13																
	G-CON-6040	GB8 Inspection - Grid L, 7-13	1d	26-Dec-23	26-Dec-23	-31d				I	GB8 Inspection - Grid L, 7-13																
	G-CON-5380	GB8 Set and Pour GB - Grid L, 7-13	3d	27-Dec-23	29-Dec-23	-31d				I	GB8 Set and Pour GB - Grid L, 7-13																
	G-CON-5670	GB8 Strip, Clean, & Move Formwork - Grid L, 7-13	1d	02-Jan-24	02-Jan-24	-31d				I	GB8 Strip, Clean, & Move Formwork - Grid L, 7-13																
	GB10 - Grid C-L, 6-8		10d	29-Dec-23	12-Jan-24	-30d																					
	G-CON-5500	GB10 Layout Grade Beams - Grid C-L, 6-8	1d	29-Dec-23	29-Dec-23	-31d				I	GB10 Layout Grade Beams - Grid C-L, 6-8																
	G-CON-5390	GB10 Form One Side of GB & Install Void Form - Grid C-L, 6-8	1d	02-Jan-24	02-Jan-24	-31d				I	GB10 Form One Side of GB & Install Void Form - Grid C-L, 6-8																
	G-CON-5410	GB10 Install Rebar for GB - Grid C-L, 6-8	2d	03-Jan-24	04-Jan-24	-30d				I	GB10 Install Rebar for GB - Grid C-L, 6-8																
	G-CON-6050	GB10 Close Form for GB - Grid C-L, 6-8	2d	05-Jan-24	08-Jan-24	-31d				I	GB10 Close Form for GB - Grid C-L, 6-8																
	G-CON-6060	GB10 Install Anchor Bolts/ Clean Up - Grid C-L, 6-8	2d	05-Jan-24	08-Jan-24	-30d				I	GB10 Install Anchor Bolts/ Clean Up - Grid C-L, 6-8																
	G-CON-6070	GB10 Inspection - Grid C-L, 6-8	1d	08-Jan-24	08-Jan-24	-30d				I	GB10 Inspection - Grid C-L, 6-8																
	G-CON-5430	GB10 Set and Pour GB - Grid C-L, 6-8	3d	09-Jan-24	11-Jan-24	-30d				I	GB10 Set and Pour GB - Grid C-L, 6-8																
	G-CON-5460	GB10 Strip, Clean, & Move Formwork - Grid C-L, 6-8	1d	12-Jan-24	12-Jan-24	-30d				I	GB10 Strip, Clean, & Move Formwork - Grid C-L, 6-8																
	GB12 - Grid A-C, 1-6		10d	03-Jan-24	16-Jan-24	-31d																					
	G-CON-7260	GB12 Layout Grade Beams - Grid A-C, 1-6	1d	03-Jan-24	03-Jan-24	-31d				I	GB12 Layout Grade Beams - Grid A-C, 1-6																
	G-CON-5420	GB12 Form One Side of GB & Install Void Form - Grid A-C, 1-	1d	04-Jan-24	04-Jan-24	-31d				I	GB12 Form One Side of GB & Install Void Form - Grid A-C, 1-6																
	G-CON-5450	GB12 Install Rebar for GB - Grid A-C, 1-6	2d	05-Jan-24	08-Jan-24	-30d				I	GB12 Install Rebar for GB - Grid A-C, 1-6																
	G-CON-6080	GB12 Close Form for GB - Grid A-C, 1-6	2d	09-Jan-24	10-Jan-24	-31d				I	GB12 Close Form for GB - Grid A-C, 1-6																
	G-CON-6090	GB12 Install Anchor Bolts/ Clean Up - Grid A-C, 1-6	2d	09-Jan-24	10-Jan-24	-31d				I	GB12 Install Anchor Bolts/ Clean Up - Grid A-C, 1-6																
	G-CON-6100	GB12 Inspection - Grid A-C, 1-6	1d	10-Jan-24	10-Jan-24	-31d				I	GB12 Inspection - Grid A-C, 1-6																
	G-CON-5470	GB12 Set and Pour GB - Grid A-C, 1-6	3d	11-Jan-24	15-Jan-24	-31d				I	GB12 Set and Pour GB - Grid A-C, 1-6																
	G-CON-5680	GB12 Strip, Clean, & Move Formwork - Grid A-C, 1-6	1d	16-Jan-24	16-Jan-24	-31d				I	GB12 Strip, Clean, & Move Formwork - Grid A-C, 1-6																
	GB14 - Grid C-M, 1		9d	15-Jan-24	25-Jan-24	104d																					
	G-CON-7580	GB14 Layout Grade Beams - Grid C-M, 1	1d	15-Jan-24	15-Jan-24	102d				I	GB14 Layout Grade Beams - Grid C-M, 1																
	G-CON-7510	GB14 Form One Side of GB & Install Void Form - Grid C-M, 1	1d	16-Jan-24	16-Jan-24	102d				I	GB14 Form One Side of GB & Install Void Form - Grid C-M, 1																
	G-CON-7520	GB14 Install Rebar for GB - Grid C-M, 1	2d	17-Jan-24	18-Jan-24	102d				I	GB14 Install Rebar for GB - Grid C-M, 1																
	G-CON-7550	GB14 Close Form for GB - Grid C-M, 1	2d	18-Jan-24	19-Jan-24	102d				I	GB14 Close Form for GB - Grid C-M, 1																
	G-CON-7560	GB14 Install Anchor Bolts/ Clean Up - Grid C-M, 1	2d	18-Jan-24	19-Jan-24	104d				I	GB14 Install Anchor Bolts/ Clean Up - Grid C-M, 1																
	G-CON-7570	GB14 Inspection - Grid C-M, 1	1d	19-Jan-24	19-Jan-24	104d				I	GB14 Inspection - Grid C-M, 1																
	G-CON-7530	GB14 Set and Pour GB - Grid C-M, 1	3d	22-Jan-24	24-Jan-24	104d				I	GB14 Set and Pour GB - Grid C-M, 1																
	G-CON-7540	GB14 Strip, Clean, & Move Formwork - Grid C-M, 1	1d	25-Jan-24	25-Jan-24	104d				I	GB14 Strip, Clean, & Move Formwork - Grid C-M, 1																
	GB15 - Grid M-Q, 1-5		10d	16-Jan-24	29-Jan-24	102d																					
	G-CON-7660	GB15 Layout Grade Beams - Grid M-Q, 1-5	1d	16-Jan-24	16-Jan-24	102d				I	GB15 Layout Grade Beams - Grid M-Q, 1-5																
	G-CON-7590	GB15 Form One Side of GB & Install Void Form - Grid M-Q, 1-	1d	17-Jan-24	17-Jan-24	102d				I	GB15 Form One Side of GB & Install Void Form - Grid M-Q, 1-5																
	G-CON-7600	GB15 Install Rebar for GB - Grid M-Q, 1-5	2d	18-Jan-24	19-Jan-24	103d				I	GB15 Install Rebar for GB - Grid M-Q, 1-5																
	G-CON-7630	GB15 Close Form for GB - Grid M-Q, 1-5	2d	22-Jan-24	23-Jan-24	102d				I	GB15 Close Form for GB - Grid M-Q, 1-5																
	G-CON-7640	GB15 Install Anchor Bolts/ Clean Up - Grid M-Q, 1-5	2d	22-Jan-24	23-Jan-24	102d				I	GB15 Install Anchor Bolts/ Clean Up - Grid M-Q, 1-5																

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

■ Remaining Level of Effort ■ Remaining Work
■ Actual Level of Effort ■ Critical Remaining ...
■ Actual Work ◆ Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	G-CON-7650	GB15 Inspection - Grid M-Q, 1-5	1d	23-Jan-24	23-Jan-24	102d																					
	G-CON-7610	GB15 Set and Pour GB - Grid M-Q, 1-5	3d	24-Jan-24	26-Jan-24	102d																					
	G-CON-7620	GB15 Strip, Clean, & Move Formwork - Grid M-Q, 1-5	1d	29-Jan-24	29-Jan-24	102d																					
	Crew 2 - Grade Beams & Pier Caps		36d	20-Nov-23	12-Jan-24	-29d																					
	PC1 - Grid M-N, 5-14		7d	20-Nov-23	30-Nov-23	-17d																					
	G-CON-7030	PC1 Layout Pier Caps - Grid M-N, 5-14	1d	20-Nov-23	20-Nov-23	-31d																					
	G-CON-7040	PC1 Formwork Pier Caps & Install Void Form - Grid M-N, 5-14	1d	21-Nov-23	21-Nov-23	-31d																					
	G-CON-7050	PC1 Install Rebar for Pier Caps - Grid M-N, 5-14	1d	22-Nov-23	22-Nov-23	-17d																					
	G-CON-7070	PC1 Install Anchor Bolts/ Clean Up - Grid M-N, 5-14	1d	27-Nov-23	27-Nov-23	-17d																					
	G-CON-7080	PC1 Inspection - Grid M-N, 5-14	1d	28-Nov-23	28-Nov-23	-17d																					
	G-CON-7090	PC1 Set and Pour Pier Caps - Grid M-N, 5-14	1d	29-Nov-23	29-Nov-23	-17d																					
	G-CON-7100	PC1 Strip, Clean, & Move Pier Caps Formwork - Grid M-N, 5-	1d	30-Nov-23	30-Nov-23	-17d																					
	GB3 - Grid R, 10-14		9d	22-Nov-23	06-Dec-23	-31d																					
	G-CON-7340	GB3 Layout Grade Beams - Grid R, 10-14	1d	22-Nov-23	22-Nov-23	-31d																					
	G-CON-7270	GB3 Form One Side of GB & Install Void Form - Grid R, 10-14	1d	27-Nov-23	27-Nov-23	-31d																					
	G-CON-7280	GB3 Install Rebar for GB - Grid R, 10-14	2d	28-Nov-23	29-Nov-23	-31d																					
	G-CON-7310	GB3 Close Form for GB - Grid R, 10-14	2d	29-Nov-23	30-Nov-23	-31d																					
	G-CON-7320	GB3 Install Anchor Bolts/ Clean Up - Grid R, 10-14	2d	29-Nov-23	30-Nov-23	-31d																					
	G-CON-7330	GB3 Inspection - Grid R, 10-14	1d	30-Nov-23	30-Nov-23	-31d																					
	G-CON-7290	GB3 Set and Pour GB - Grid R, 10-14	3d	01-Dec-23	05-Dec-23	-31d																					
	G-CON-7300	GB3 Strip, Clean, & Move Formwork - Grid R, 10-14	1d	06-Dec-23	06-Dec-23	-31d																					
	GB5 - Grid N-R, 14-16		10d	27-Nov-23	08-Dec-23	-29d																					
	G-CON-7420	GB5 Layout Grade Beams - Grid N-R, 14-16	1d	27-Nov-23	27-Nov-23	-31d																					
	G-CON-7350	GB5 Form One Side of GB & Install Void Form - Grid N-R, 14-	1d	28-Nov-23	28-Nov-23	-31d																					
	G-CON-7360	GB5 Install Rebar for GB - Grid N-R, 14-16	2d	29-Nov-23	30-Nov-23	-28d																					
	G-CON-7390	GB5 Close Form for GB - Grid N-R, 14-16	2d	01-Dec-23	04-Dec-23	-29d																					
	G-CON-7400	GB5 Install Anchor Bolts/ Clean Up - Grid N-R, 14-16	2d	01-Dec-23	04-Dec-23	-29d																					
	G-CON-7410	GB5 Inspection - Grid N-R, 14-16	1d	04-Dec-23	04-Dec-23	-29d																					
	G-CON-7370	GB5 Set and Pour GB - Grid N-R, 14-16	3d	05-Dec-23	07-Dec-23	-29d																					
	G-CON-7380	GB5 Strip, Clean, & Move Formwork - Grid N-R, 14-16	1d	08-Dec-23	08-Dec-23	-29d																					
	GB7 - Grid J.1-P, 14-16		9d	07-Dec-23	19-Dec-23	-28d																					
	G-CON-7500	GB7 Layout Grade Beams - Grid J.1-P, 14-16	1d	07-Dec-23	07-Dec-23	-31d																					
	G-CON-7430	GB7 Form One Side of GB & Install Void Form - Grid J.1-P, 14	1d	08-Dec-23	08-Dec-23	-31d																					
	G-CON-7440	GB7 Install Rebar for GB - Grid J.1-P, 14-16	2d	11-Dec-23	12-Dec-23	-31d																					
	G-CON-7470	GB7 Close Form for GB - Grid J.1-P, 14-16	2d	12-Dec-23	13-Dec-23	-31d																					
	G-CON-7480	GB7 Install Anchor Bolts/ Clean Up - Grid J.1-P, 14-16	2d	12-Dec-23	13-Dec-23	-28d																					
	G-CON-7490	GB7 Inspection - Grid J.1-P, 14-16	1d	13-Dec-23	13-Dec-23	-28d																					
	G-CON-7450	GB7 Set and Pour GB - Grid J.1-P, 14-16	3d	14-Dec-23	18-Dec-23	-28d																					
	G-CON-7460	GB7 Strip, Clean, & Move Formwork - Grid J.1-P, 14-16	1d	19-Dec-23	19-Dec-23	-28d																					
	GB9 - Grid J.1-L, 10-14		11d	11-Dec-23	26-Dec-23	-31d																					
	G-CON-7740	GB9 Layout Grade Beams - Grid J.1-L, 10-14	1d	11-Dec-23	11-Dec-23	-29d																					
	G-CON-7670	GB9 Form One Side of GB & Install Void Form - Grid J.1-L, 10	1d	14-Dec-23	14-Dec-23	-31d																					
	G-CON-7680	GB9 Install Rebar for GB - Grid J.1-L, 10-14	2d	15-Dec-23	18-Dec-23	-31d																					
	G-CON-7710	GB9 Close Form for GB - Grid J.1-L, 10-14	2d	18-Dec-23	19-Dec-23	-31d																					
	G-CON-7720	GB9 Install Anchor Bolts/ Clean Up - Grid J.1-L, 10-14	2d	18-Dec-23	19-Dec-23	-31d																					
	G-CON-7730	GB9 Inspection - Grid J.1-L, 10-14	1d	19-Dec-23	19-Dec-23	-31d																					
	G-CON-7690	GB9 Set and Pour GB - Grid J.1-L, 10-14	3d	20-Dec-23	22-Dec-23	-31d																					
	G-CON-7700	GB9 Strip, Clean, & Move Formwork - Grid J.1-L, 10-14	1d	26-Dec-23	26-Dec-23	-31d																					
	PC11 - Grid B-L, 3-5		7d	26-Dec-23	04-Jan-24	-31d																					

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

■ Remaining Level of Effort ■ Remaining Work
■ Actual Level of Effort ■ Critical Remaining ...
■ Actual Work ◆ Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025										
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3	
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul
	G-CON-7110	PC11 Layout Pier Caps - Grid B-L, 3-5	1d	26-Dec-23	26-Dec-23	-31d																						
	G-CON-7120	PC11 Formwork Pier Caps & Install Void Form - Grid B-L, 3-5	1d	27-Dec-23	27-Dec-23	-31d																						
	G-CON-7130	PC11 Install Rebar for Pier Caps - Grid B-L, 3-5	1d	28-Dec-23	28-Dec-23	-31d																						
	G-CON-7140	PC11 Install Anchor Bolts/ Clean Up - Grid B-L, 3-5	1d	29-Dec-23	29-Dec-23	-31d																						
	G-CON-7150	PC11 Inspection - Grid B-L, 3-5	1d	02-Jan-24	02-Jan-24	-31d																						
	G-CON-7160	PC11 Set and Pour Pier Caps - Grid B-L, 3-5	1d	03-Jan-24	03-Jan-24	-31d																						
	G-CON-7170	PC11 Strip, Clean, & Move Pier Caps Formwork - Grid B-L, 3-	1d	04-Jan-24	04-Jan-24	-31d																						
	PC13 - Grid L-N, 2-4		7d	04-Jan-24	12-Jan-24	-29d																						
	G-CON-7180	PC13 Layout Pier Caps - Grid L-N, 2-4	1d	04-Jan-24	04-Jan-24	-29d																						
	G-CON-7190	PC13 Formwork Pier Caps & Install Void Form - Grid L-N, 2-4	1d	05-Jan-24	05-Jan-24	-29d																						
	G-CON-7200	PC13 Install Rebar for Pier Caps - Grid L-N, 2-4	1d	08-Jan-24	08-Jan-24	-29d																						
	G-CON-7210	PC13 Install Anchor Bolts/ Clean Up - Grid L-N, 2-4	1d	09-Jan-24	09-Jan-24	-29d																						
	G-CON-7220	PC13 Inspection - Grid L-N, 2-4	1d	10-Jan-24	10-Jan-24	-29d																						
	G-CON-7230	PC13 Set and Pour Pier Caps - Grid L-N, 2-4	1d	11-Jan-24	11-Jan-24	-29d																						
	G-CON-7240	PC13 Strip, Clean, & Move Pier Caps Formwork - Grid L-N, 2-	1d	12-Jan-24	12-Jan-24	-29d																						
	SOG		181d	19-Dec-23	03-Sep-24	-6d																						
	SOG Pour #1 Grid L-Q, 10-15		23d	19-Dec-23	22-Jan-24	-27d																						
	G-CON-6110	Backfill & Rough Grade - SOG 1 - Grid L-Q, 10-15	5d	19-Dec-23	26-Dec-23	-29d																						
	G-CON-6160	Granular Fill - SOG 1 - Grid L-Q, 10-15	4d	27-Dec-23	02-Jan-24	-29d																						
	G-CON-1610	Electrical in Slab - SOG 1 - Grid L-Q, 10-15	3d	03-Jan-24	05-Jan-24	-27d																						
	G-CON-6800	Plumbing in Slab - SOG 1 - Grid L-Q, 10-15	3d	03-Jan-24	05-Jan-24	-27d																						
	G-CON-1070	Install Vapor Barrier - SOG 1 - Grid L-Q, 10-15	4d	08-Jan-24	11-Jan-24	-27d																						
	G-CON-1550	Set Edge Form < 1' & Column Blockouts - SOG 1 - Grid L-Q,	5d	09-Jan-24	15-Jan-24	-27d																						
	G-CON-1560	Install Rebar & Slip Dowels - SOG 1 - Grid L-Q, 10-15	4d	12-Jan-24	17-Jan-24	-27d																						
	G-CON-1570	Install Hanging Form & Depressions - SOG 1 - Grid L-Q, 10-15	3d	16-Jan-24	18-Jan-24	-27d																						
	G-CON-1580	Inspection & Clean Up - SOG 1 - Grid L-Q, 10-15	1d	18-Jan-24	18-Jan-24	-27d																						
	G-CON-1590	Pour SOG - SOG 1 - Grid L-Q, 10-15	1d	19-Jan-24	19-Jan-24	-27d																						
	G-CON-1240	Pour Waste Slab for Tilt - South & West	1d	22-Jan-24	22-Jan-24	-27d																						
	G-CON-1600	Strip/ Clean C.J. & Patch Vapor Barrier - SOG 1 - Grid L-Q, 10-	1d	22-Jan-24	22-Jan-24	-27d																						
	SOG Pour #2 Grid L-A, 6-1		26d	05-Jan-24	09-Feb-24	-30d																						
	G-CON-6120	Backfill & Rough Grade - SOG 2 - Grid L-A, 6-1	5d	05-Jan-24	11-Jan-24	-31d																						
	G-CON-1040	Granular Fill - SOG 2 - Grid L-A, 6-1	4d	12-Jan-24	17-Jan-24	-31d																						
	G-CON-6650	Electrical in Slab - SOG 2 - Grid L-A, 6-1	3d	18-Jan-24	22-Jan-24	-31d																						
	G-CON-6810	Plumbing in Slab - SOG 2 - Grid L-A, 6-1	3d	18-Jan-24	22-Jan-24	-31d																						
	G-CON-6170	Install Vapor Barrier - SOG 2 - Grid L-A, 6-1	4d	23-Jan-24	26-Jan-24	-31d																						
	G-CON-6180	Set Edge Form < 1' & Column Blockouts - SOG 2 - Grid L-A, 6-	5d	26-Jan-24	01-Feb-24	-31d																						
	G-CON-6190	Install Rebar & Slip Dowels - SOG 2 - Grid L-A, 6-1	4d	31-Jan-24	05-Feb-24	-31d																						
	G-CON-6200	Install Hanging Form & Depressions - SOG 2 - Grid L-A, 6-1	3d	02-Feb-24	06-Feb-24	-31d																						
	G-CON-6210	Inspection & Clean Up - SOG 2 - Grid L-A, 6-1	1d	06-Feb-24	06-Feb-24	-31d																						
	G-CON-6220	Pour SOG - SOG 2 - Grid L-A, 6-1	1d	07-Feb-24	07-Feb-24	-31d																						
	G-CON-6240	Pour Waste Slab for Tilt - Northwest	1d	08-Feb-24	08-Feb-24	-31d																						
	G-CON-6230	Strip/ Clean C.J. & Patch Vapor Barrier - SOG 2 - Grid L-A, 6-1	2d	08-Feb-24	09-Feb-24	-30d																						
	SOG Pour #3 Grid L-Q, 10-1		28d	17-Jan-24	23-Feb-24	-31d																						
	G-CON-6130	Backfill & Rough Grade - SOG 3 - Grid L-Q, 10-1	5d	17-Jan-24	23-Jan-24	-31d																						
	G-CON-7760	Granular Fill - SOG 3 - Grid L-Q, 10-1	4d	24-Jan-24	29-Jan-24	-31d																						
	G-CON-6670	Electrical in Slab - SOG 3 - Grid L-Q, 10-1	3d	30-Jan-24	01-Feb-24	-31d																						
	G-CON-6820	Plumbing in Slab - SOG 3 - Grid L-Q, 10-1	3d	30-Jan-24	01-Feb-24	-31d																						
	G-CON-6260	Install Vapor Barrier - SOG 3 - Grid L-Q, 10-1	5d	02-Feb-24	08-Feb-24	-31d																						
	G-CON-6270	Set Edge Form < 1' & Column Blockouts - SOG 3 - Grid L-Q,	7d	07-Feb-24	15-Feb-24	-31d																						

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

■ Remaining Level of Effort ■ Remaining Work
■ Actual Level of Effort ■ Critical Remaining ...
■ Actual Work ◆ Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
	G-CON-6280	Install Rebar & Slip Dowels - SOG 3 - Grid L-Q, 10-1	6d	12-Feb-24	19-Feb-24	-31d																					
	G-CON-6290	Install Hanging Form & Depressions - SOG 3 - Grid L-Q, 10-1	4d	14-Feb-24	19-Feb-24	-31d																					
	G-CON-6300	Inspection & Clean Up - SOG 3 - Grid L-Q, 10-1	1d	19-Feb-24	19-Feb-24	-31d																					
	G-CON-6310	Pour SOG - SOG 3 - Grid L-Q, 10-1	1d	20-Feb-24	20-Feb-24	-31d																					
	G-CON-6330	Pour Waste Slab for Tilt - North	1d	21-Feb-24	21-Feb-24	-31d																					
	G-CON-6320	Strip/ Clean C.J. & Patch Vapor Barrier - SOG 3 - Grid L-Q, 10-1	3d	21-Feb-24	23-Feb-24	-31d																					
	SOG Pour #4 (After Steel)		25d	23-Jul-24	26-Aug-24	-2d																					
	G-CON-7810	Plumbing Perimeter Trench Drain - Pour 4	6d	23-Jul-24	30-Jul-24	-6d																					
	G-CON-7830	Backfill Perimeter Trench Drain - Pour 4	3d	31-Jul-24	02-Aug-24	-4d																					
	G-CON-6850	Plumbing in Slab - Pour 4	4d	06-Aug-24	09-Aug-24	-5d																					
	G-CON-6510	Install Vapor Barrier - Pour 4	4d	12-Aug-24	15-Aug-24	-5d																					
	G-CON-6520	Set Edge Form < 1' & Column Blockouts - Pour 4	4d	13-Aug-24	16-Aug-24	-5d																					
	G-CON-6530	Install Rebar & Slip Dowels - Pour 4	4d	16-Aug-24	21-Aug-24	-5d																					
	G-CON-6540	Install Hanging Form & Depressions - Pour 4	3d	20-Aug-24	22-Aug-24	-4d																					
	G-CON-6550	Inspection & Clean Up - Pour 4	1d	22-Aug-24	22-Aug-24	-2d																					
	G-CON-6560	Pour SOG - Pour 4	1d	23-Aug-24	23-Aug-24	-2d																					
	G-CON-6570	Strip/ Clean C.J. & Patch Vapor Barrier - Pour 4	1d	26-Aug-24	26-Aug-24	-2d																					
	SOG Pour #5 (After Steel)		24d	31-Jul-24	03-Sep-24	-6d																					
	G-CON-7820	Plumbing Perimeter Trench Drain - Pour 5	6d	31-Jul-24	07-Aug-24	-6d																					
	G-CON-7840	Backfill Perimeter Trench Drain - Pour 5	3d	08-Aug-24	12-Aug-24	-6d																					
	G-CON-6860	Plumbing in Slab - Pour 5	4d	13-Aug-24	16-Aug-24	-6d																					
	G-CON-6580	Install Vapor Barrier - Pour 5	4d	19-Aug-24	22-Aug-24	-6d																					
	G-CON-6590	Set Edge Form < 1' & Column Blockouts - Pour 5	4d	20-Aug-24	23-Aug-24	-6d																					
	G-CON-6600	Install Rebar & Slip Dowels - Pour 5	4d	23-Aug-24	28-Aug-24	-6d																					
	G-CON-6610	Install Hanging Form & Depressions - Pour 5	3d	27-Aug-24	29-Aug-24	-6d																					
	G-CON-6620	Inspection & Clean Up - Pour 5	1d	29-Aug-24	29-Aug-24	-6d																					
	G-CON-6630	Pour SOG - Pour 5	1d	30-Aug-24	30-Aug-24	-6d																					
	G-CON-6640	Strip/ Clean C.J. & Patch Vapor Barrier - Pour 5	1d	03-Sep-24	03-Sep-24	-6d																					
	Tilt Structure		148d	23-Jan-24	19-Aug-24	5d																					
	Tilt Pour #01 Panels 1-21		31d	23-Jan-24	05-Mar-24	9d																					
	G-STRT-1000	Layout Tilt Wall Panels - Panels 1-21	3d	23-Jan-24	25-Jan-24	-27d																					
	G-CON-1250	Form Tilt Wall Panels - Panels 1-21	8d	25-Jan-24	05-Feb-24	-27d																					
	G-CON-1630	Prep Slab & Install Embeds - Panels 1-21	5d	30-Jan-24	05-Feb-24	8d																					
	G-STRT-1020	Install Wire Mesh Arch Panel - Panels 1-21	3d	06-Feb-24	08-Feb-24	8d																					
	G-STRT-1080	Pour Arch Panel Install Insulation - Panels 1-21	1d	09-Feb-24	09-Feb-24	8d																					
	G-STRT-1090	Rebar Struct Panel - Panels 1-21	8d	12-Feb-24	21-Feb-24	8d																					
	G-STRT-1030	MEP/Embeds/Pick Inserts/ Brace Inserts - Panels 1-21	7d	14-Feb-24	22-Feb-24	8d																					
	G-STRT-1040	Pour Struct Panel - Panels 1-21	1d	27-Feb-24	27-Feb-24	8d																					
	G-STRT-1050	Cure Tilt Wall Panels - Panels 1-21	5d	28-Feb-24	05-Mar-24	9d																					
	Tilt Pour #02 Panels 22-41		28d	09-Feb-24	19-Mar-24	-1d																					
	G-CON-6255	Layout Tilt Wall Panels - Panels 22-41	3d	09-Feb-24	13-Feb-24	-31d																					
	G-CON-5810	Form Tilt Wall Panels - Panels 22-41	8d	13-Feb-24	22-Feb-24	-31d																					
	G-CON-6340	Prep Slab & Install Embeds - Panels 22-41	5d	16-Feb-24	22-Feb-24	-1d																					
	G-STRT-1100	Install Wire Mesh Arch Panel - Panels 22-41	2d	23-Feb-24	26-Feb-24	-1d																					
	G-STRT-1110	Pour Arch Panel Install Insulation - Panels 22-41	1d	27-Feb-24	27-Feb-24	-1d																					
	G-STRT-1120	Rebar Struct Panel - Panels 22-41	8d	28-Feb-24	08-Mar-24	-1d																					
	G-STRT-1130	MEP/Embeds/Pick Inserts/ Brace Inserts - Panels 22-41	7d	01-Mar-24	11-Mar-24	-1d																					
	G-STRT-1060	Pour Struct Panel - Panels 22-41	1d	12-Mar-24	12-Mar-24	-1d																					
	G-STRT-1070	Cure Tilt Wall Panels - Panels 22-41	5d	13-Mar-24	19-Mar-24	-1d																					

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

■ Remaining Level of Effort ■ Remaining Work
■ Actual Level of Effort ■ Critical Remaining ...
■ Actual Work ◆ Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
	Tilt Pour #03 Panels 42-62	29d	22-Feb-24	02-Apr-24	-11d																						
G-CON-6950	Layout Tilt Wall Panels - Panels 42-62	3d	22-Feb-24	26-Feb-24	-31d																						
G-CON-5820	Form Tilt Wall Panels - Panels 42-62	8d	26-Feb-24	06-Mar-24	-31d																						
G-CON-6960	Prep Slab & Install Embeds - Panels 42-62	5d	29-Feb-24	06-Mar-24	-11d																						
G-STRT-1140	Install Wire Mesh Arch Panel - Panels 42-62	3d	07-Mar-24	11-Mar-24	-11d																						
G-STRT-1150	Pour Arch Panel Install Insulation - Panels 42-62	1d	12-Mar-24	12-Mar-24	-11d																						
G-STRT-1160	Rebar Struct Panel - Panels 42-62	8d	13-Mar-24	22-Mar-24	-11d																						
G-STRT-1170	MEP/Embeds/Pick Inserts/ Brace Inserts - Panels 42-62	7d	15-Mar-24	25-Mar-24	-11d																						
G-STRT-1180	Pour Struct Panel - Panels 42-62	1d	26-Mar-24	26-Mar-24	-11d																						
G-STRT-1190	Cure Tilt Wall Panels - Panels 42-62	5d	27-Mar-24	02-Apr-24	-11d																						
	Tilt Pour #04 Panels 63-81	29d	06-Mar-24	15-Apr-24	-20d																						
G-CON-6970	Layout Tilt Wall Panels - Panels 63-81	3d	06-Mar-24	08-Mar-24	-31d																						
G-CON-5830	Form Tilt Wall Panels - Panels 63-81	8d	08-Mar-24	19-Mar-24	-31d																						
G-CON-6980	Prep Slab & Install Embeds - Panels 63-81	5d	13-Mar-24	19-Mar-24	-20d																						
G-STRT-1200	Install Wire Mesh Arch Panel - Panels 63-81	3d	20-Mar-24	22-Mar-24	-20d																						
G-STRT-1210	Pour Arch Panel Install Insulation - Panels 63-81	1d	25-Mar-24	25-Mar-24	-20d																						
G-STRT-1220	Rebar Struct Panel - Panels 63-81	8d	26-Mar-24	04-Apr-24	-20d																						
G-STRT-1230	MEP/Embeds/Pick Inserts/ Brace Inserts - Panels 63-81	7d	28-Mar-24	05-Apr-24	-20d																						
G-STRT-1240	Pour Struct Panel - Panels 63-81	1d	08-Apr-24	08-Apr-24	-20d																						
G-STRT-1250	Cure Tilt Wall Panels - Panels 63-81	5d	09-Apr-24	15-Apr-24	-20d																						
	Tilt Pour #05 Panels 82-100	30d	19-Mar-24	29-Apr-24	-29d																						
G-CON-6990	Layout Tilt Wall Panels - Panels 82-100	3d	19-Mar-24	21-Mar-24	-31d																						
G-CON-5840	Form Tilt Wall Panels - Panels 82-100	8d	22-Mar-24	02-Apr-24	-31d																						
G-CON-7000	Prep Slab & Install Embeds - Panels 82-100	5d	27-Mar-24	02-Apr-24	-29d																						
G-STRT-1260	Install Wire Mesh Arch Panel - Panels 82-100	3d	03-Apr-24	05-Apr-24	-29d																						
G-STRT-1270	Pour Arch Panel Install Insulation - Panels 82-100	1d	08-Apr-24	08-Apr-24	-29d																						
G-STRT-1280	Rebar Struct Panel - Panels 82-100	8d	09-Apr-24	18-Apr-24	-29d																						
G-STRT-1290	MEP/Embeds/Pick Inserts/ Brace Inserts - Panels 82-100	7d	11-Apr-24	19-Apr-24	-29d																						
G-STRT-1300	Pour Struct Panel - Panels 82-100	1d	22-Apr-24	22-Apr-24	-29d																						
G-STRT-1310	Cure Tilt Wall Panels - Panels 82-100	5d	23-Apr-24	29-Apr-24	-29d																						
	Tilt Pour #06 Panels 101-106	19d	02-Apr-24	26-Apr-24	-29d																						
G-CON-7010	Layout Tilt Wall Panels - Panels 101-106	1d	02-Apr-24	02-Apr-24	-31d																						
G-CON-5850	Form Tilt Wall Panels - Panels 101-106	3d	03-Apr-24	05-Apr-24	-31d																						
G-CON-7020	Prep Slab & Install Embeds - Panels 101-106	2d	05-Apr-24	08-Apr-24	-31d																						
G-STRT-1320	Install Wire Mesh Arch Panel - Panels 101-106	2d	09-Apr-24	10-Apr-24	-31d																						
G-STRT-1330	Pour Arch Panel Install Insulation - Panels 101-106	1d	11-Apr-24	11-Apr-24	-31d																						
G-STRT-1340	Rebar Struct Panel - Panels 101-106	3d	12-Apr-24	16-Apr-24	-31d																						
G-STRT-1350	MEP/Embeds/Pick Inserts/ Brace Inserts - Panels 101-106	3d	16-Apr-24	18-Apr-24	-31d																						
G-STRT-1360	Pour Struct Panel - Panels 101-106	1d	19-Apr-24	19-Apr-24	-31d																						
G-STRT-1370	Cure Tilt Wall Panels - Panels 101-106	5d	22-Apr-24	26-Apr-24	-29d																						
	Tilt Structure	84d	22-Apr-24	19-Aug-24	5d																						
G-CON-1680	Prep for Tilt Erection	5d	22-Apr-24	26-Apr-24	-31d																						
G-CON-1690	Mobilize & Assemble Crane	2d	29-Apr-24	30-Apr-24	-31d																						
G-CON-1360	Erect Tilt Panels	8d	01-May-24	10-May-24	-31d																						
G-CON-1700	Disassemble & Mob-Out Crane	2d	13-May-24	14-May-24	-15d																						
G-CON-1410	Layout Walls & MEP Main Runs	5d	13-May-24	17-May-24	39d																						
G-CON-7750	Electrical Rough-in in Pour Back Strips	5d	01-Jul-24	08-Jul-24	-11d																						
G-CON-1370	Backfill & Base Perimeter Strip	15d	24-Jun-24	15-Jul-24	-21d																						
G-CON-1720	Plumbing Rough-in in Pour Back Strips	15d	01-Jul-24	22-Jul-24	-21d																						

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul
	G-CON-1260	F/R/P/S Perimeter SOG Pour Back & Column Diamonds	10d	23-Jul-24	05-Aug-24	-21d																					
	G-CON-1110	Masonry Walls (Incll Door Frames)	15d	30-Jul-24	19-Aug-24	-10d																					
	G-CON-5020	MEP Rough-in CMU Walls	15d	30-Jul-24	19-Aug-24	5d																					
	Structural Steel		59d	13-May-24	05-Aug-24	92d																					
	Steel - Lot 1 Grid 1-10, Q-N		16d	13-May-24	04-Jun-24	-31d																					
	G-CON-1440	Steel - Set Crane	2d	13-May-24	14-May-24	-31d																					
	G-CON-1980	Steel - Enabling Work - Lot 1 Grid 1-10, Q-N	3d	13-May-24	15-May-24	-31d																					
	G-CON-1280	Steel - Erect Columns & Framing - Lot 1 Grid 1-10, Q-N	5d	15-May-24	21-May-24	-31d																					
	G-CON-1090	Steel - Decking & Detailing - Lot 1 Grid 1-10, Q-N	10d	21-May-24	04-Jun-24	-31d																					
	Steel - Lot 2 Grid 10-16, R-N		21d	16-May-24	14-Jun-24	-31d																					
	G-CON-8090	Steel - Enabling Work - Lot 2 Grid 10-16, R-N	3d	16-May-24	20-May-24	-26d																					
	G-CON-8100	Steel - Erect Columns & Framing - Lot 2 Grid 10-16, R-N	5d	22-May-24	29-May-24	-28d																					
	G-CON-8110	Steel - Decking & Detailing - Lot 2 Grid 10-16, R-N	10d	03-Jun-24	14-Jun-24	-31d																					
	Steel - Lot 3 Grid 16-10, N-J		20d	21-May-24	18-Jun-24	-31d																					
	G-CON-8120	Steel - Enabling Work - Lot 3 Grid 16-10, N-J	3d	21-May-24	23-May-24	-24d																					
	G-CON-8140	Steel - Erect Columns & Framing - Lot 3 Grid 16-10, N-J	3d	30-May-24	03-Jun-24	-28d																					
	G-CON-8160	Steel - Decking & Detailing - Lot 3 Grid 16-10, N-J	7d	10-Jun-24	18-Jun-24	-31d																					
	Steel - Mezzanine - Lot 8 Grid 4-1, N-L		35d	04-Jun-24	23-Jul-24	-29d																					
	G-CON-5100	Steel - Mezzanine Columns & Framing - Lot 8 Grid 4-1, N-L	3d	04-Jun-24	06-Jun-24	-28d																					
	G-CON-8240	Steel - Mezzanine Decking & Detailing - Lot 8 Grid 4-1, N-L	6d	09-Jul-24	16-Jul-24	-29d																					
	G-CON-8290	Concrete - Rebar & Pour Mezzanine	5d	17-Jul-24	23-Jul-24	-29d																					
	Steel - Lot 4 Grid 10-3, N-L		22d	24-May-24	25-Jun-24	-31d																					
	G-CON-8130	Steel - Enabling Work - Lot 4 Grid 10-3, N-L	3d	24-May-24	29-May-24	-21d																					
	G-CON-8150	Steel - Erect Columns & Framing - Lot 4 Grid 10-3, N-L	3d	07-Jun-24	11-Jun-24	-28d																					
	G-CON-8170	Steel - Decking & Detailing - Lot 4 Grid 10-3, N-L	7d	17-Jun-24	25-Jun-24	-31d																					
	Steel - Lot 5 Grid L-A, 6-3		24d	30-May-24	02-Jul-24	-29d																					
	G-CON-8180	Steel - Enabling Work - Lot 5 Grid L-A, 6-3	3d	30-May-24	03-Jun-24	-17d																					
	G-CON-8200	Steel - Erect Columns & Framing - Lot 5 Grid 6-3, L-A	3d	12-Jun-24	14-Jun-24	-24d																					
	G-CON-8220	Steel - Decking & Detailing - Lot 5 Grid L-A, 6-3	7d	24-Jun-24	02-Jul-24	-29d																					
	Steel - Lot 6 Grid 3-1, M-A		26d	04-Jun-24	10-Jul-24	-29d																					
	G-CON-8190	Steel - Enabling Work - Lot 6 Grid 3-1, M-A	3d	04-Jun-24	06-Jun-24	-15d																					
	G-CON-8210	Steel - Erect Columns & Framing - Lot 6 Grid 3-1, M-A	3d	17-Jun-24	19-Jun-24	-22d																					
	G-CON-8230	Steel - Decking & Detailing - Lot 6 Grid 3-1, M-A	7d	01-Jul-24	10-Jul-24	-29d																					
	Steel - Eyebrow - Lot 7 Grid 10-3, N-L		41d	07-Jun-24	05-Aug-24	92d																					
	G-CON-8250	Steel - Enabling Work - Eyebrow - Lot 7 Grid 10-3, N-L	4d	07-Jun-24	12-Jun-24	113d																					
	G-CON-8260	Steel - Erect Columns & Framing - Eyebrow - Lot 7 Grid 10-3, N-L	5d	20-Jun-24	26-Jun-24	106d																					
	G-CON-8270	Steel - Decking & Detailing - Eyebrow - Lot 7 Grid 10-3, N-L	15d	16-Jul-24	05-Aug-24	92d																					
	Roof / Skin Finishes		73d	05-Jun-24	17-Sep-24	86d																					
	Roof - Zone 1 Grid 16-12		42d	19-Jun-24	16-Aug-24	-1d																					
	G-CON-5120	Elect - Stubups (Incll Lightning Protection) - Z1 Grids 16-12	2d	19-Jun-24	20-Jun-24	-14d																					
	G-CON-5080	HVAC - Set Roof Curbs - Z1 Grids 16-12	3d	19-Jun-24	21-Jun-24	-15d																					
	G-CON-5110	Plumb Stub Ups - Z1 Grids 16-12	3d	19-Jun-24	21-Jun-24	-15d																					
	G-CON-1100	Roofing - Z1 Grids 16-12	10d	24-Jun-24	08-Jul-24	-15d																					
	G-CON-5040	Set HVAC Gear - Z1 Grids 16-12	2d	15-Aug-24	16-Aug-24	-1d																					
	Roof - Zone 2 Grid 12-7		39d	26-Jun-24	20-Aug-24	-1d																					
	G-CON-7860	Elect - Stubups (Incll Lightning Protection)- Z2 Grid 12-7	2d	26-Jun-24	27-Jun-24	-9d																					
	G-CON-7850	HVAC - Set Roof Curbs - Z2 Grid 12-7	3d	26-Jun-24	28-Jun-24	-10d																					
	G-CON-7870	Plumb Stub Ups - Z2 Grid 12-7	3d	26-Jun-24	28-Jun-24	-10d																					
	G-CON-8350	Roofing - Z2 Grid 12-7	10d	09-Jul-24	22-Jul-24	-15d																					

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025									
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
G-CON-7880	Set HVAC Gear - Z2 Grid 12-7	2d	19-Aug-24	20-Aug-24	-1d																						
Roof - Zone 3 Grid 7-1		31d	11-Jul-24	22-Aug-24	-1d																						
G-CON-7890	HVAC - Set Roof Curbs - Z3 Grid 7-1	2d	11-Jul-24	12-Jul-24	-9d																						
G-CON-7910	Plumb Stub Ups - Z3 Grid 7-1	2d	11-Jul-24	12-Jul-24	-9d																						
G-CON-7900	Elect - Stubups (Incl Lightning Protection)- Z3 Grid 7-1	2d	11-Jul-24	12-Jul-24	-9d																						
G-CON-8360	Roofing - Z3 Grid 7-1	11d	23-Jul-24	06-Aug-24	-15d																						
G-CON-7920	Set HVAC Gear - Z3 Grid 7-1	2d	21-Aug-24	22-Aug-24	-1d																						
Roof - Zone 4 Grid J-A		59d	05-Jun-24	27-Aug-24	-1d																						
G-CON-7970	Paint Booth Exhaust / Roof Stub Ups - Z4 Grid J-A	3d	05-Jun-24	07-Jun-24	41d																						
G-CON-7950	Plumb Stub Ups - Z4 Grid J-A	2d	15-Jul-24	16-Jul-24	15d																						
G-CON-7940	Elect - Stubups (Incl Lightning Protection)- Z4 Grid J-A	2d	15-Jul-24	16-Jul-24	15d																						
G-CON-7930	HVAC - Set Roof Curbs - Z4 Grid J-A	4d	15-Jul-24	18-Jul-24	13d																						
G-CON-8370	Roofing - Z4 Grid J-A	11d	07-Aug-24	21-Aug-24	0d																						
G-CON-7960	Set HVAC Gear - Z4 Grid J-A	3d	23-Aug-24	27-Aug-24	-1d																						
Roof / Skin Finishes		73d	05-Jun-24	17-Sep-24	86d																						
G-CON-1350	Exterior Framing / Support Steel for Insulated Core Metal Panels	15d	05-Jun-24	25-Jun-24	3d																						
G-CON-1620	Electrical Rough-in at Storefront	4d	26-Jun-24	01-Jul-24	4d																						
G-CON-1330	Storefront (Includes Entry Doors with Card Readers)	15d	02-Jul-24	23-Jul-24	4d																						
G-CON-1390	Exterior Coating	20d	16-Jul-24	12-Aug-24	5d																						
G-CON-1310	Insulated Core Metal Panels	15d	24-Jul-24	13-Aug-24	4d																						
G-CON-1400	Glass / Glazing in Wall Panels	10d	14-Aug-24	27-Aug-24	4d																						
G-CON-8030	Electrical Exterior Trim & Lighting	15d	13-Aug-24	03-Sep-24	72d																						
G-CON-8280	Steel - Stairs & Bollards	8d	04-Sep-24	13-Sep-24	88d																						
G-CON-1320	Illuminated Signage	10d	04-Sep-24	17-Sep-24	72d																						
Interior Buildout		156d	17-Jun-24	28-Jan-25	-5d																						
Rough-in		124d	17-Jun-24	11-Dec-24	13d																						
Rough-in - Zone 1 Grid 16-12		123d	17-Jun-24	10-Dec-24	14d																						
Rough-in - Zone 1 Grid 16-12		72d	17-Jun-24	26-Sep-24	-4d																						
G-RI-P-1000	Fire Sprinkler Overhead Rough-in - Mains / Homeruns	6d	17-Jun-24	24-Jun-24	-31d																						
G-RI-P-1020	HVAC Duct Overhead Rough-in	7d	25-Jun-24	03-Jul-24	-31d																						
G-RI-P-1010	Electrical Overhead Rough-in - Mains / Homeruns	15d	17-Jun-24	08-Jul-24	-28d																						
G-RI-P-1130	Fire Sprinkler Overhead Rough-in - Branches	12d	25-Jun-24	11-Jul-24	-9d																						
G-RI-P-1050	Frame Priority Rooms ER, IDF, PPE (1116, 1115, 1120)	3d	16-Jul-24	18-Jul-24	-21d																						
G-RI-P-1060	Hang Drywall Priority Rooms ER, IDF, PPE (1116, 1115, 1120)	2d	19-Jul-24	22-Jul-24	4d																						
G-RI-P-1030	HVAC Pipe Overhead Rough-in	14d	02-Jul-24	22-Jul-24	-31d																						
G-RI-P-1040	Plumbing Overhead Rough-in - Drains / Vents / Water	12d	05-Jul-24	22-Jul-24	-24d																						
G-RI-P-1090	Frame Walls (Including Door Frames)	4d	23-Jul-24	26-Jul-24	-23d																						
G-RI-P-1070	Tape & Finish Priority Rooms ER, IDF, PPE (1116, 1115, 1120)	4d	23-Jul-24	26-Jul-24	4d																						
G-RI-P-1140	HVAC Duct & Pipe Testing	5d	23-Jul-24	29-Jul-24	-17d																						
G-RI-P-1080	Prime & First Coat Paint Priority Rooms ER, IDF, PPE (1116, 1115, 1120)	2d	29-Jul-24	30-Jul-24	4d																						
G-RI-P-1410	Plumbing Overhead Rough-in - Gas - Including Loading Bay P	10d	23-Jul-24	05-Aug-24	-22d																						
G-RI-P-1100	I/W Plumbing Rough-in	4d	01-Aug-24	06-Aug-24	-23d																						
G-RI-P-1430	Plumbing Pipe Testing	5d	07-Aug-24	13-Aug-24	-21d																						
G-RI-P-1160	Prime & 1st Coat Paint - Structural, MEP	7d	06-Aug-24	14-Aug-24	-22d																						
G-RI-P-1170	Hang Drywall	4d	15-Aug-24	20-Aug-24	-22d																						
G-RI-P-1120	HVAC - Equipment (Hose Kits, IR Heaters, Unit Heaters, Etc -	10d	15-Aug-24	28-Aug-24	-14d																						
G-RI-P-1180	Tape & Finish Drywall	8d	21-Aug-24	30-Aug-24	-22d																						
G-RI-P-1190	Prime & 1st Coat Paint - Walls & Finishes	8d	03-Sep-24	12-Sep-24	-19d																						
G-RI-P-1200	Electrical Branch / Surface Mount (Incl Fire Alarm)	10d	13-Sep-24	26-Sep-24	-4d																						

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort
 Actual Level of Effort
 Actual Work
 Remaining Work
 Critical Remaining ...
 Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024																		2025					
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3		
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun			
	Provo ER - West Electrical Room 16M - GUB-01-1116	82d	31-Jul-24	22-Nov-24	-15d																								
	G-RI-ER116-1000 Set Equipment - GUB-01-1116	4d	31-Jul-24	05-Aug-24	4d																								
	G-RI-ER116-1010 Rough-in Conduit - GUB-01-1116	10d	06-Aug-24	19-Aug-24	8d																								
	G-RI-ER116-1020 Pull & Term Wire - GUB-01-1116	10d	20-Aug-24	03-Sep-24	8d																								
	G-RI-ER116-1030 Testing & Energization - GUB-01-1116	1d	22-Nov-24	22-Nov-24	-15d																								
	Provo PPE - PPE Storage Room - GUB-01-3C-1120	82d	31-Jul-24	22-Nov-24	-15d																								
	G-RI-ER116-1040 Set Equipment - GUB-01-3C-1120	4d	31-Jul-24	05-Aug-24	4d																								
	G-RI-ER116-1050 Rough-in Conduit - GUB-01-3C-1120	10d	06-Aug-24	19-Aug-24	8d																								
	G-RI-ER116-1060 Pull & Term Wire - GUB-01-3C-1120	10d	20-Aug-24	03-Sep-24	8d																								
	G-RI-ER116-1070 Testing & Energization - GUB-01-3C-1120	1d	22-Nov-24	22-Nov-24	-15d																								
	Provo - IDF Room GUB-01-1115	88d	06-Aug-24	10-Dec-24	14d																								
	G-RI-ER115-1000 Set Equipment - GUB-01-1115	4d	06-Aug-24	09-Aug-24	4d																								
	G-RI-ER115-1010 Rough-in Conduit - GUB-01-1115	10d	12-Aug-24	23-Aug-24	4d																								
	G-RI-ER115-1020 Pull & Term Wire - GUB-01-1115	10d	26-Aug-24	09-Sep-24	4d																								
	G-RI-ER115-1030 Testing & Energization - GUB-01-1115	1d	02-Dec-24	02-Dec-24	-15d																								
	G-CON-8580 Startup Splits - GUB-01-1115	3d	03-Dec-24	05-Dec-24	0d																								
	G-RI-ER115-1040 Owner IT Equip - GUB-01-1115	3d	06-Dec-24	10-Dec-24	14d																								
	Rough-in - Zone 2 Grid 12-7	88d	28-Jun-24	31-Oct-24	-19d																								
	G-RI-P-1210 Fire Sprinkler Overhead Rough-in - Mains / Homeruns	6d	28-Jun-24	08-Jul-24	-31d																								
	G-RI-P-1280 Electrical Overhead Rough-in - Mains / Homeruns	15d	09-Jul-24	29-Jul-24	-28d																								
	G-RI-P-1330 HVAC Duct Overhead Rough-in	15d	09-Jul-24	29-Jul-24	-31d																								
	G-RI-P-1400 Fire Sprinkler Overhead Rough-in - Branches	12d	12-Jul-24	29-Jul-24	-9d																								
	G-RI-P-1340 HVAC Pipe Overhead Rough-in	10d	23-Jul-24	05-Aug-24	-31d																								
	G-RI-P-1390 HVAC Duct & Pipe Testing	5d	06-Aug-24	12-Aug-24	-19d																								
	G-RI-P-1350 Plumbing Overhead Rough-in - Drains / Vents / Water	12d	30-Jul-24	14-Aug-24	-29d																								
	G-RI-P-1420 Plumbing Overhead Rough-in - Gas	10d	06-Aug-24	19-Aug-24	-24d																								
	G-RI-P-1240 Frame Walls (Including Door Frames)	11d	06-Aug-24	20-Aug-24	-29d																								
	G-RI-P-1470 Frame Ceilings	2d	21-Aug-24	22-Aug-24	-20d																								
	G-RI-P-1250 I/W Electrical Rough-in	5d	21-Aug-24	27-Aug-24	-23d																								
	G-RI-P-1230 Prime & 1st Coat Paint - Structural, MEP	7d	20-Aug-24	28-Aug-24	-24d																								
	G-RI-P-1360 I/W Plumbing Rough-in	10d	15-Aug-24	28-Aug-24	-29d																								
	G-RI-P-1440 Plumbing Pipe Testing	5d	29-Aug-24	05-Sep-24	-29d																								
	G-RI-P-1380 HVAC - Equipment (Hose Kits, IR Heaters, Unit Heaters, Etc -	10d	29-Aug-24	12-Sep-24	-14d																								
	G-RI-P-1260 Hang Drywall Walls	8d	06-Sep-24	17-Sep-24	-29d																								
	G-RI-P-1480 Hang Drywall Ceilings	2d	18-Sep-24	19-Sep-24	-13d																								
	G-RI-P-1270 Tape & Finish Drywall Walls	15d	12-Sep-24	02-Oct-24	-29d																								
	G-RI-P-1490 Tape & Finish Drywall Ceilings	3d	03-Oct-24	07-Oct-24	-22d																								
	G-RI-P-1220 Prime & 1st Coat Paint - Walls & Ceilings	11d	03-Oct-24	17-Oct-24	-25d																								
	G-RI-P-1370 Electrical Branch / Surface Mount	10d	18-Oct-24	31-Oct-24	-19d																								
	Rough-in - Zone 3 Grid 7-1	106d	12-Jul-24	11-Dec-24	13d																								
	Rough-in - Zone 3 Grid 7-1	83d	12-Jul-24	06-Nov-24	-31d																								
	G-RI-A-1010 Fire Sprinkler Overhead Rough-in - Mains / Homeruns	10d	12-Jul-24	25-Jul-24	-29d																								
	G-RI-A-1060 Frame Priority Rooms ER, MDF, IDF (1011, 1013, 1223)	5d	26-Jul-24	01-Aug-24	-14d																								
	G-RI-A-1080 Fire Sprinkler Overhead Rough-in - Branches	8d	30-Jul-24	08-Aug-24	0d																								
	G-RI-A-1090 Hang Drywall Priority Rooms ER, MDF, IDF (1011, 1013, 1223	4d	07-Aug-24	12-Aug-24	-15d																								
	G-RI-A-1000 Electrical Overhead Rough-in - Mains / Homeruns	12d	30-Jul-24	14-Aug-24	-28d																								
	G-RI-A-1020 HVAC Equipment & Duct Overhead Rough-in	15d	30-Jul-24	19-Aug-24	-31d																								
	G-RI-A-1030 HVAC Pipe Overhead Rough-in - Mains	10d	06-Aug-24	19-Aug-24	-31d																								
	G-RI-A-1130 Tape & Finish Priority Rooms ER, MDF, IDF (1011, 1013, 1223	8d	13-Aug-24	22-Aug-24	-15d																								

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
G-RI-P-1450	HVAC Duct & PipeTesting	5d	20-Aug-24	26-Aug-24	-12d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024																	2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
G-RI-FP1017-1020 G-RI-FP1017-1030 G-RI-FP1017-1040 GSE - IDF Room GUB-01-1223 G-RI-ER1223-100 G-RI-ER1223-100 G-RI-ER1223-100 G-RI-ER1223-100 G-CON-1830 G-RI-ER1223-100 Rough-in - Zone 4 Grid J-A Rough-in - Zone 4 Grid J-A G-RI-G-1010 G-RI-G-1000 G-RI-G-1120 G-RI-G-1020 G-RI-G-1030 G-RI-G-1040 G-RI-G-1140 G-RI-G-1050 G-RI-G-1060 G-RI-G-1090 G-RI-G-1210 G-RI-G-1220 G-RI-G-1070 G-RI-G-1160 G-RI-G-1080 G-RI-G-1150 G-RI-G-1170 G-RI-G-1230 G-RI-G-1100 G-RI-G-1180 G-RI-G-1240 G-RI-G-1190 G-RI-G-1200 GSE ER - North Electrical Room 2D - GUB-01-1216 G-RI-ER1216-100 G-RI-ER1216-100 G-RI-ER1216-100 G-RI-ER1216-100 Finishes - Zone 1 Grid 16-12 G-FN-P-1000 G-FN-P-1010 G-FN-P-1040 G-FN-P-1020 G-FN-P-1130 G-FN-P-1030 G-FN-P-1050 G-FN-P-1060	G-RI-FP1017-1020 Rough-in Conduit - GUB-01-1017	10d	09-Oct-24	22-Oct-24	-7d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																</

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

■ Remaining Level of Effort ■ Remaining Work
■ Actual Level of Effort ■ Critical Remaining ...
■ Actual Work ◆ Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024																		2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
G-FN-P-1070 G-FN-P-1090 G-FN-P-1100 G-FN-P-1110 G-FN-P-1120 G-FN-P-1150 G-FN-P-1080 G-FN-P-1160 G-FN-P-1170 G-FN-P-1180 G-FN-P-1190 G-FN-P-1210 G-FN-P-1260 G-FN-P-1580 G-FN-P-1200 G-FN-P-1240 G-FN-P-1250 G-FN-P-1230 G-FN-P-1220 G-FN-P-1270 G-FN-P-1280 Finishes - Zone 2 Grid 12-7 G-FN-P-1520 G-FN-P-1410 G-FN-P-1390 G-FN-P-1430 G-FN-P-1560 G-FN-P-1360 G-FN-P-1470 G-FN-P-1340 G-FN-P-1540 G-FN-P-1310 G-FN-P-1400 G-FN-P-1570 G-FN-P-1510 G-FN-P-1480 G-FN-P-1420 G-FN-P-1590 G-FN-P-1350 G-FN-P-1500 G-FN-P-1330 G-FN-P-1530 G-FN-P-1290 G-FN-P-1490 G-FN-P-1550 G-FN-P-1460 G-FN-P-1380 G-FN-P-1440 G-FN-P-1370	Install Baler & Misc Equipment	10d	13-Sep-24	26-Sep-24	-9d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN

INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun		Jul																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
G-FN-P-1450	Clean / Polish Concrete	10d	30-Dec-24	13-Jan-25	6d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								</

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN
INTERNAL Remaining Activities



23 of 25

Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			tr 3																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
	G-FN-G-1210	Final Paint	5d	15-Jan-25	21-Jan-25	-31d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

■ Remaining Level of Effort ■ Remaining Work
■ Actual Level of Effort ■ Critical Remaining ...
■ Actual Work ◆ Milestone

SWA GUB DEN
INTERNAL Remaining Activities



Activity ID	Activity Name	Orig Dur	Start	Finish	Total Float	2024												2025										
						Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3	
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	
<div></div>	G-CON-1760	Test & Balance - Wet (Entire Building) Pumps, Boilers, HWU	5d	07-Jan-25	13-Jan-25	-25d																						
	G-CON-1770	Test & Balance - Air - CRAC & Split Units	2d	22-Jan-25	23-Jan-25	-31d																						
	G-CON-1780	Test & Balance - Air - AHU, HVU, HRHVU, VAVs	6d	24-Jan-25	31-Jan-25	-31d																						
	G-CON-1790	Test & Balance - Air - Exhaust Fans	6d	03-Feb-25	10-Feb-25	-31d																						
	G-CON-1800	Test & Balance - Final Building Balance	2d	11-Feb-25	12-Feb-25	-31d																						
	Commissioning		20d	13-Feb-25	12-Mar-25	37d																						
	G-CON-1990	HVAC Submit & Review Test & Balance Report	10d	13-Feb-25	26-Feb-25	-31d																						
	G-CON-1940	Sequence of Operations / Final Commissioning	20d	13-Feb-25	12-Mar-25	37d																						
	Substantial Completion		47d	27-Feb-25	02-May-25	0d																						
	G-CON-1170	Final Inspections (TCO)	5d	27-Feb-25	05-Mar-25	-31d																						
	G-CON-1180	Punchlist & Corrections	10d	06-Mar-25	19-Mar-25	-31d																						
	G-CON-1190	Removal of Temp AOA	2d	20-Mar-25	21-Mar-25	-31d																						
	G-CON-1420	Owner Supplied Furniture & Office Equipment - Install	10d	20-Mar-25	02-Apr-25	22d																						
	G-CON-1200	Weather	15d	24-Mar-25	11-Apr-25	-31d																						
	G-CON-1210	*Milestone: Substantial Completion	0d		11-Apr-25*	-31d																						
	G-CON-1530	Owner Move-in, Finalize & Prep for Beneficial Occupancy	15d	14-Apr-25	02-May-25	0d																						
	G-CON-1540	*Milestone: Beneficial Occupancy	0d		02-May-25	0d																						
	Close Out		30d	05-May-25	16-Jun-25	0d																						
	Final Closeout		30d	05-May-25	16-Jun-25	0d																						
	G-CON-1220	Closeout / Final Completion	30d	05-May-25	16-Jun-25	0d																						

Run Date - 03-Oct-23
Start Date - 27-May-22
Finish Date - 16-Jun-25
Data Date - 25-Sep-23

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining ...
 Actual Work  Milestone

SWA GUB DEN
INTERNAL Remaining Activities

